


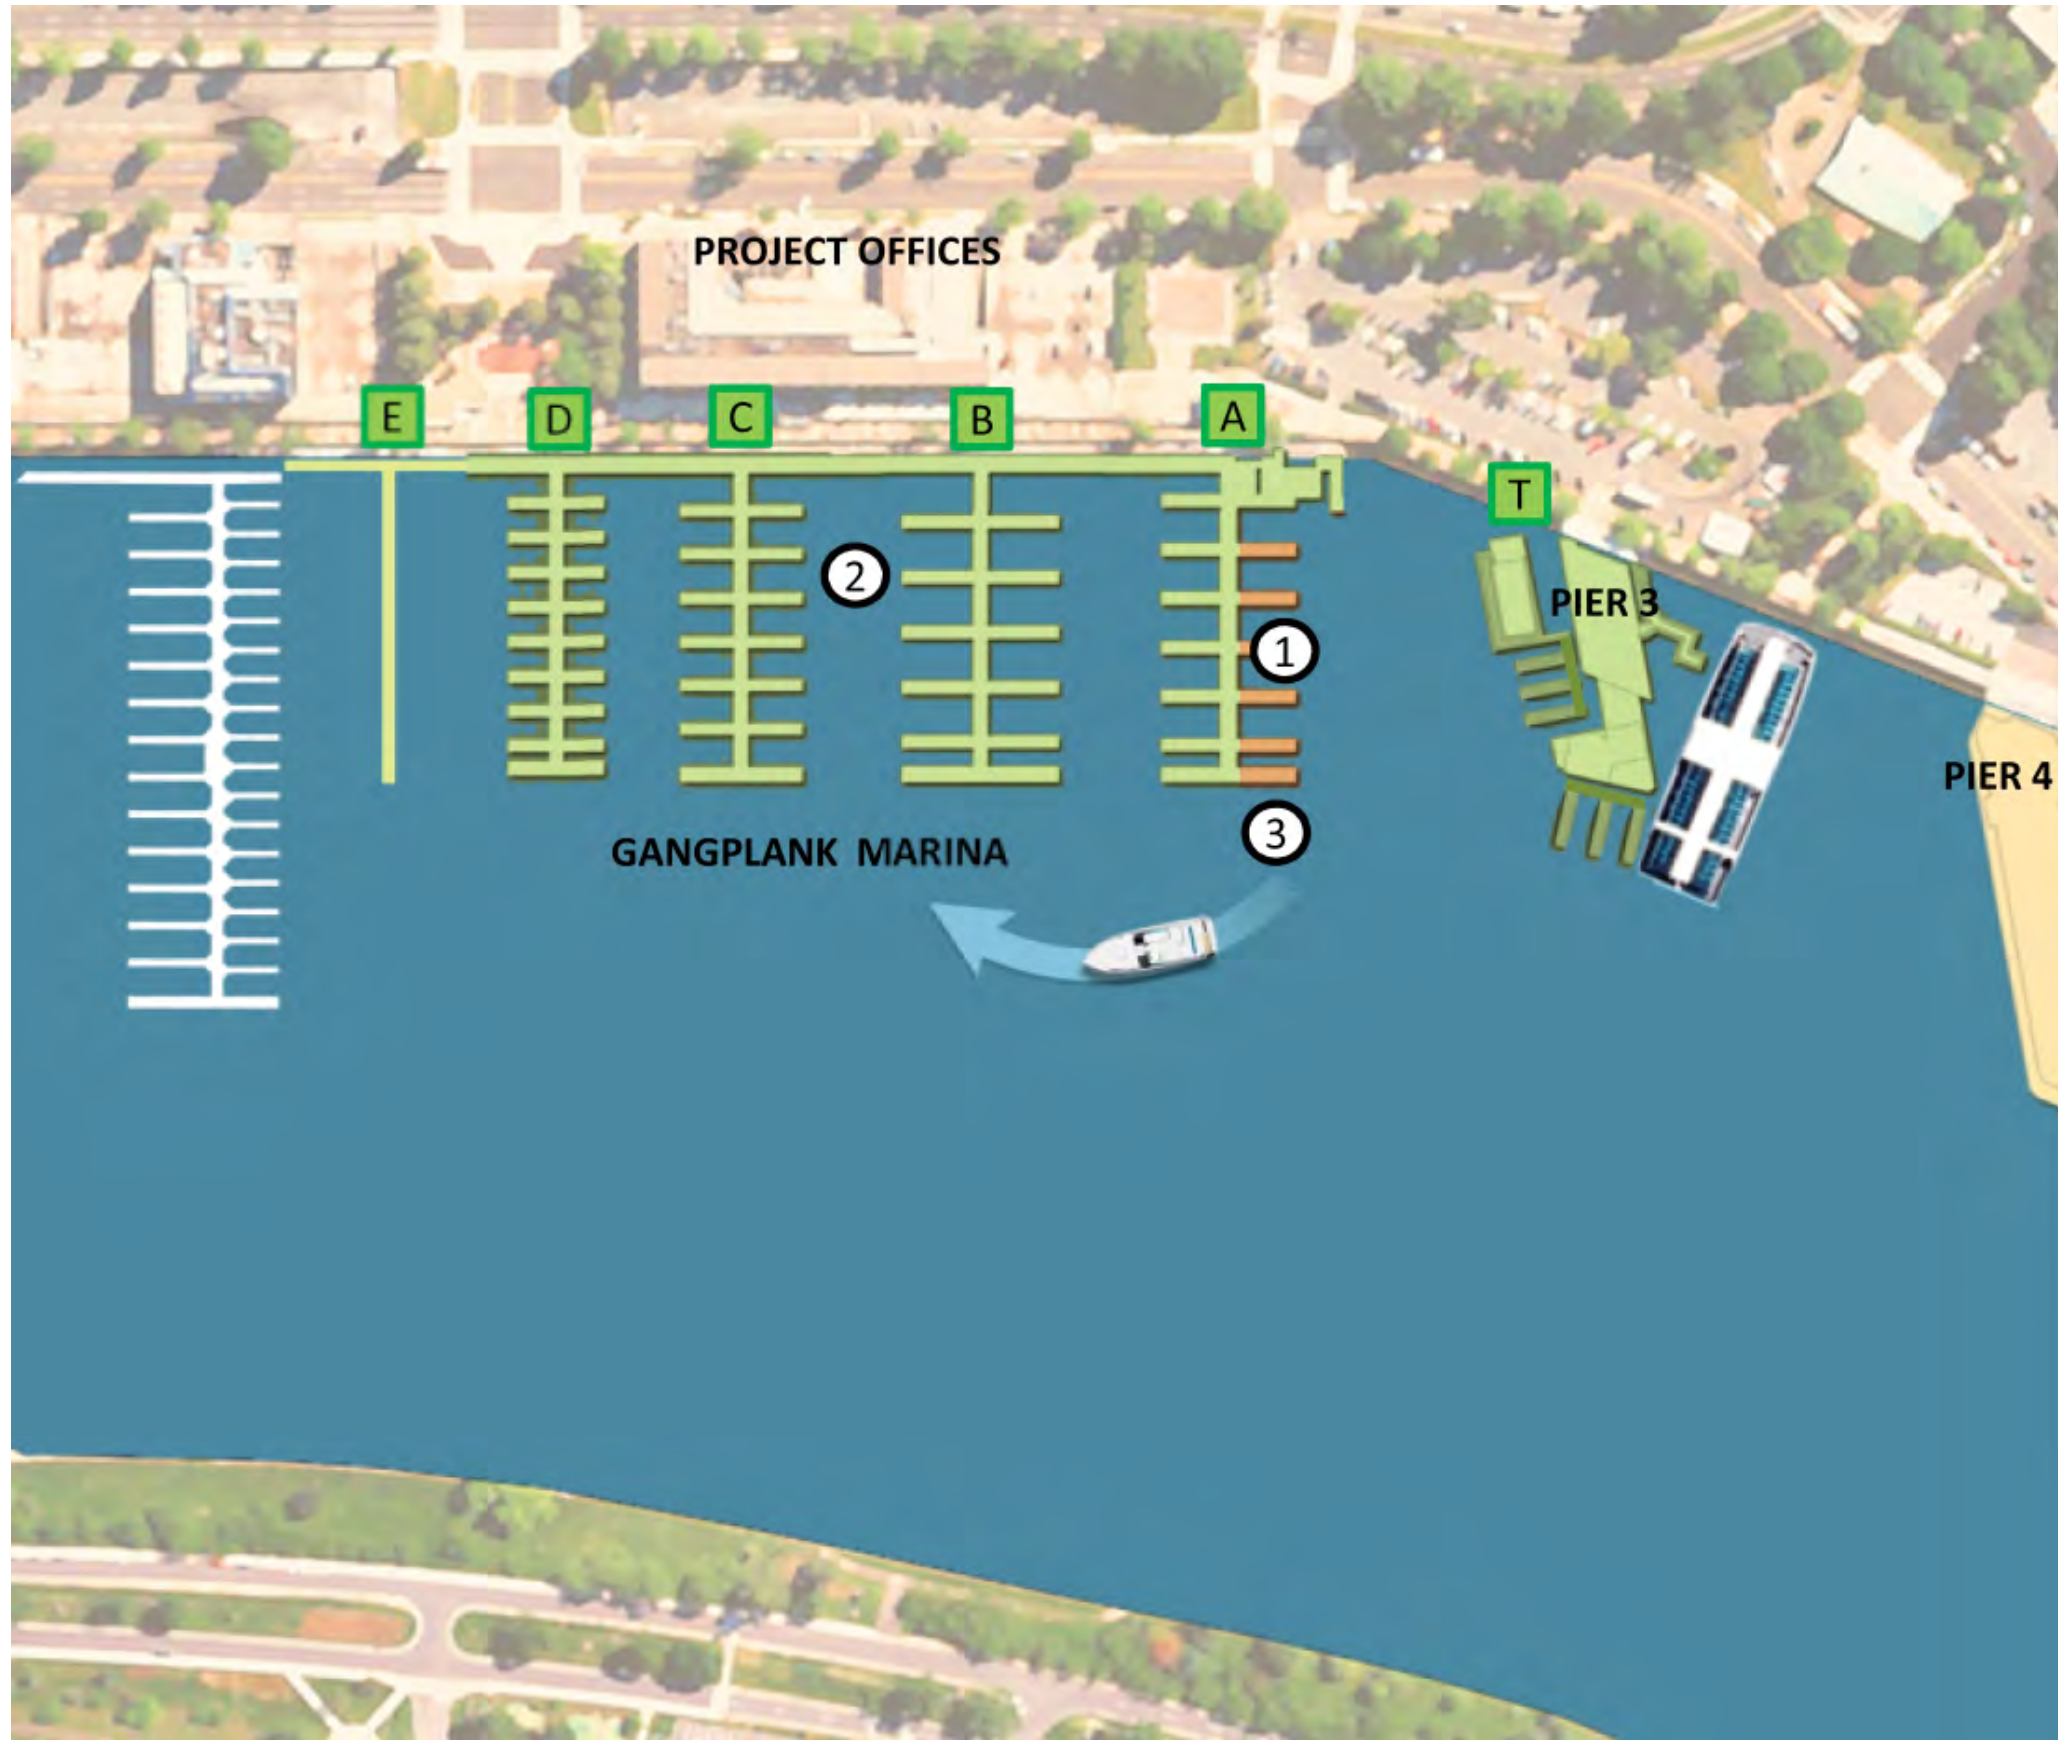


Construction

1. Demo east half of A Dock

Operations

2. Maintain vessels in Gangplank & Pier 3
3. Relocate east half of A Dock boats to empty slips in GPM

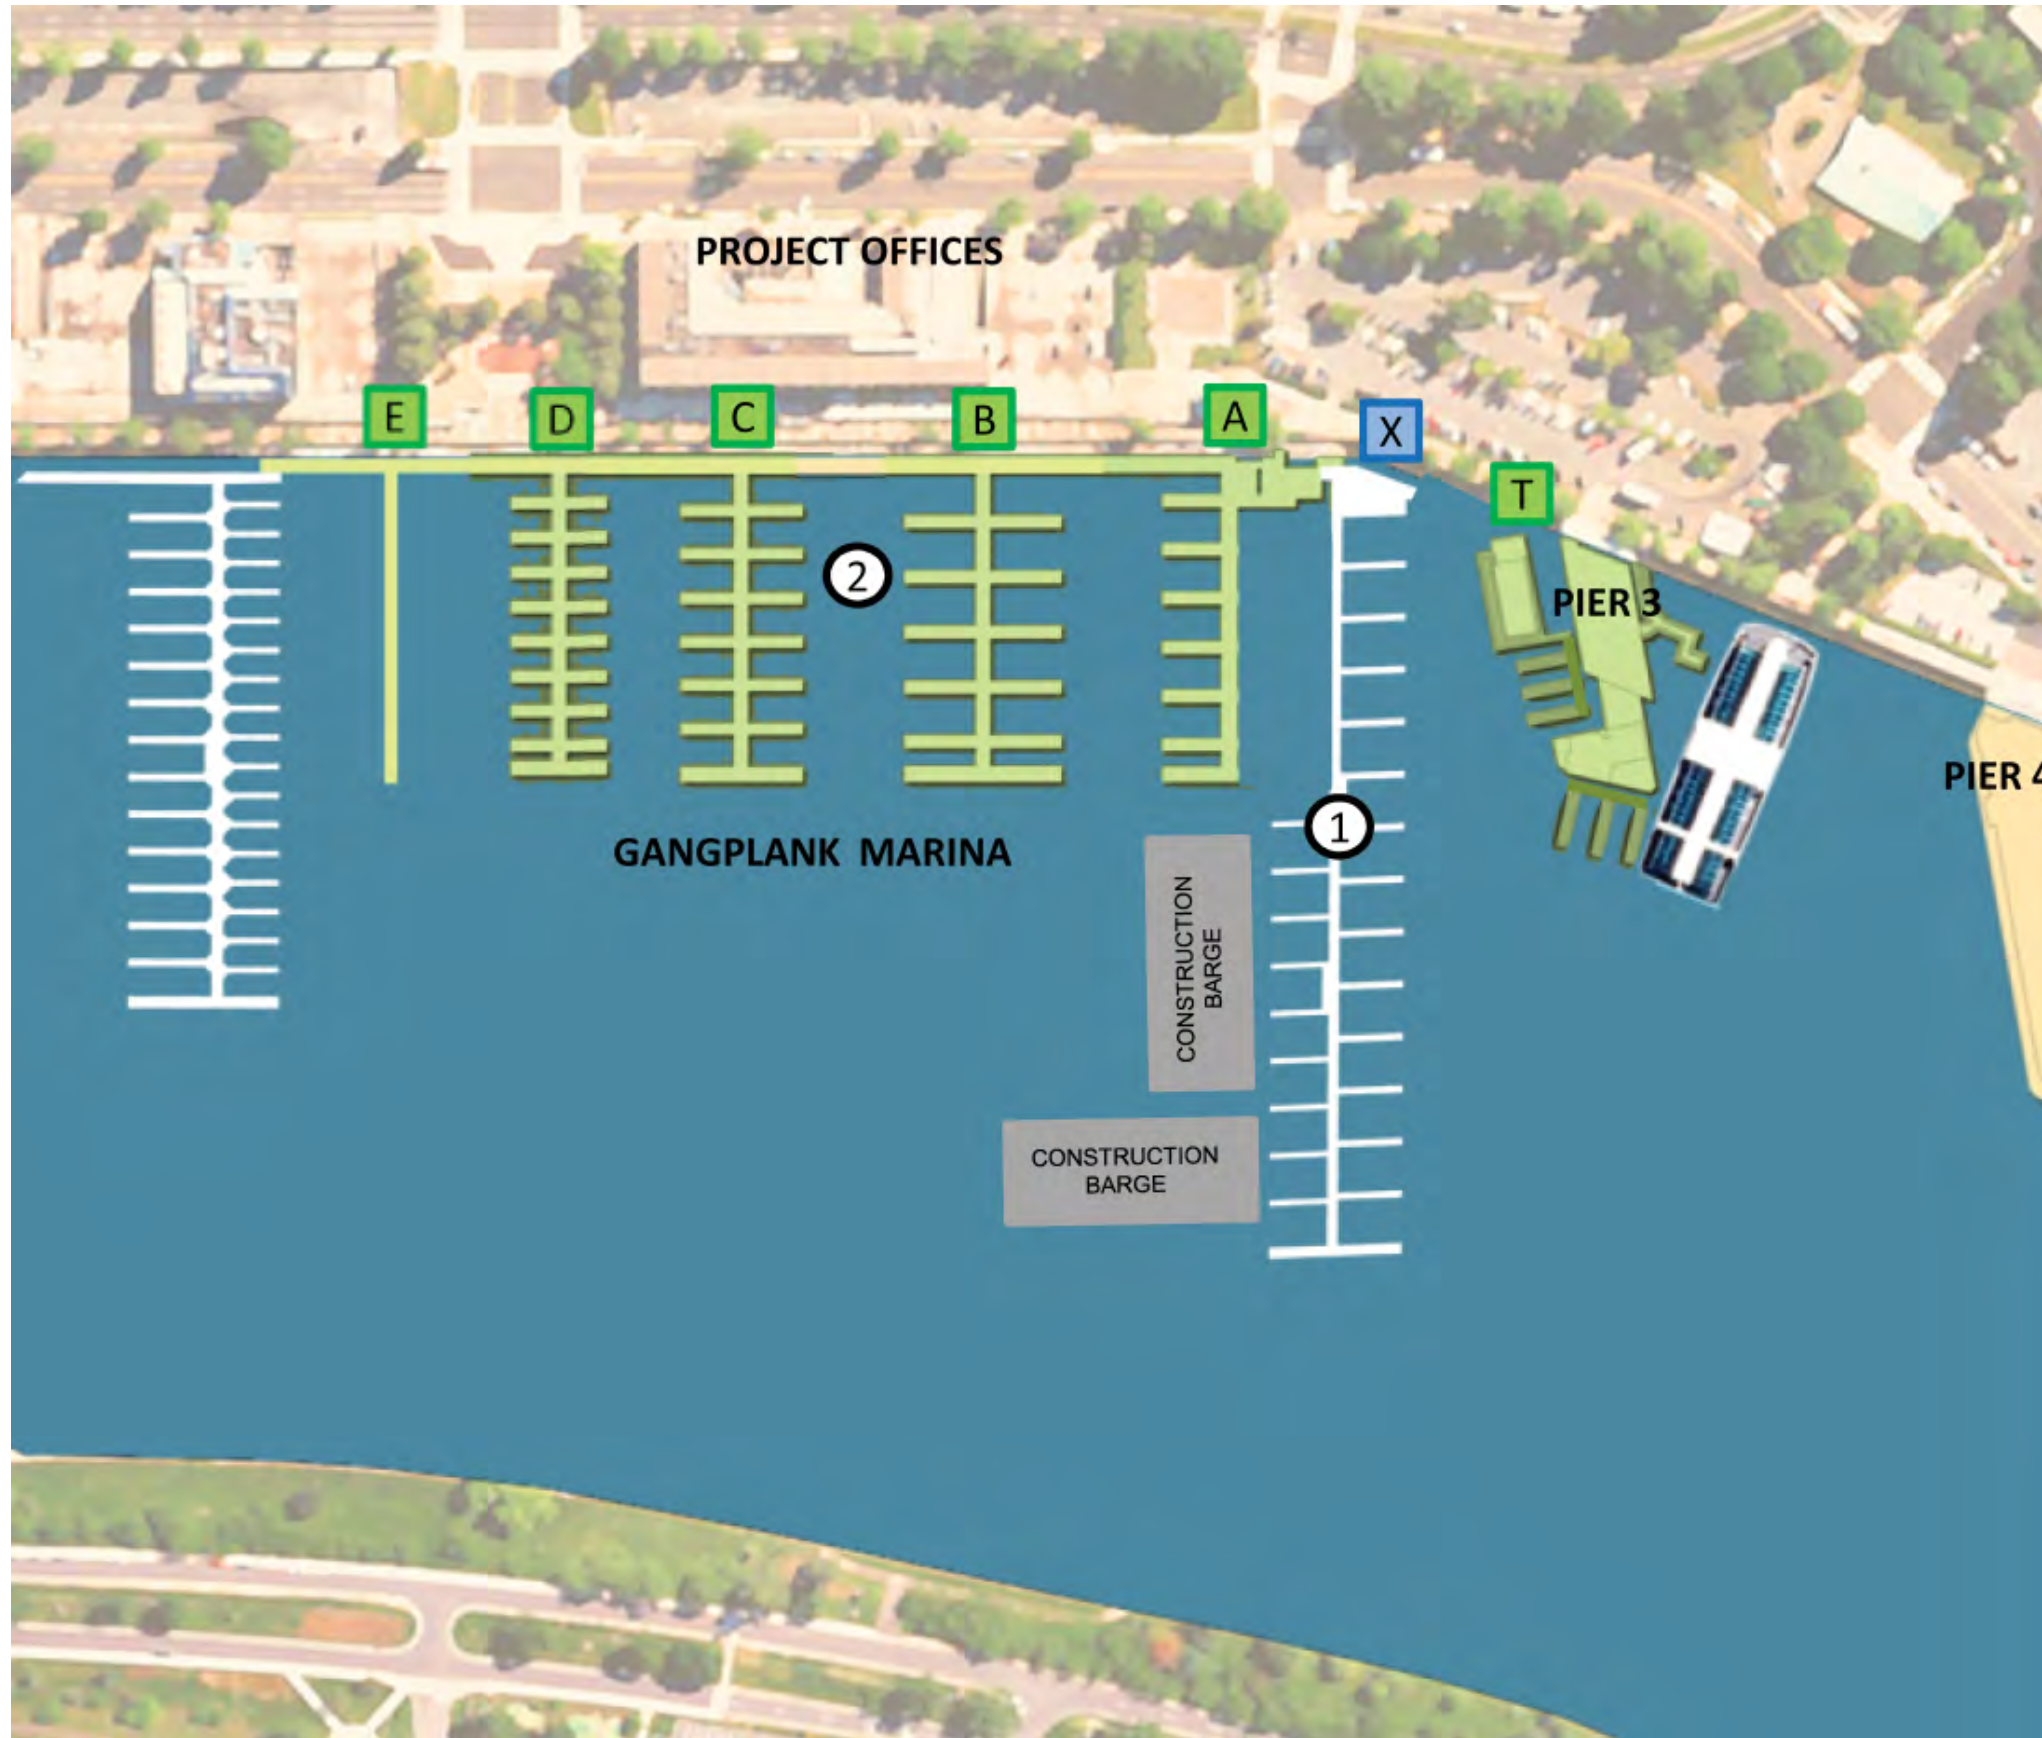


Construction

1. GPM X Dock construction

Operations

2. Maintain vessels in Gangplank & Pier 3

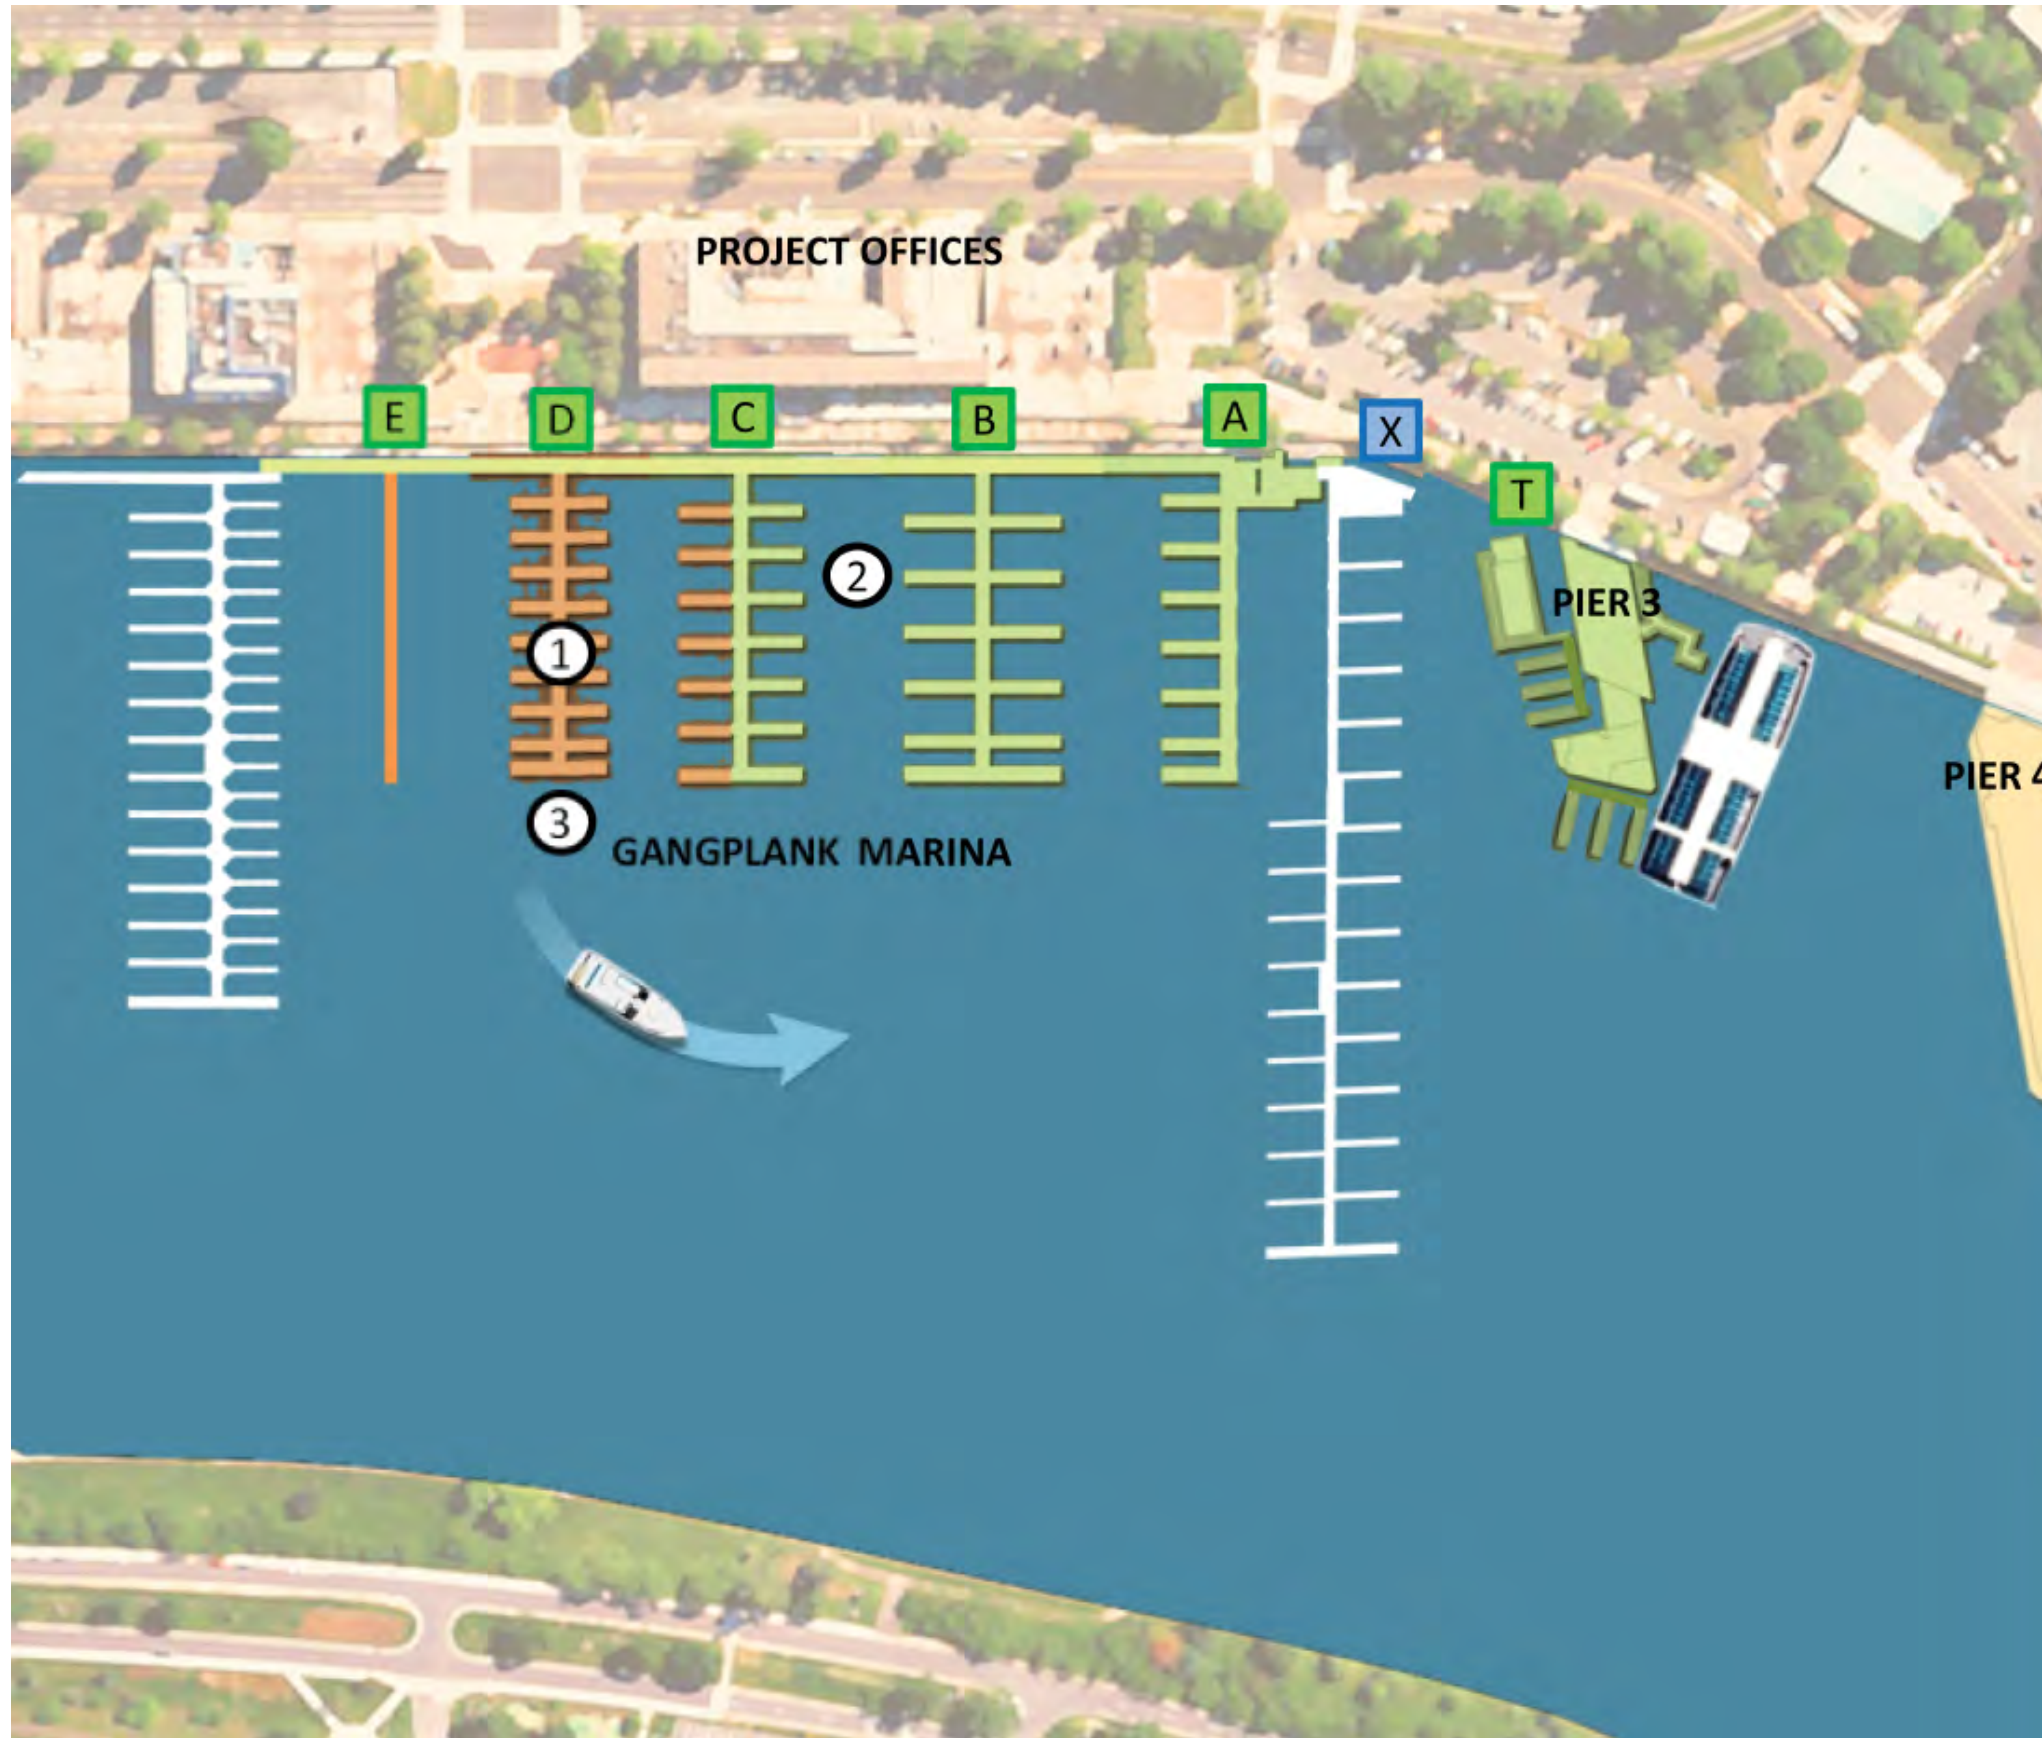


Construction

1. Demo GPM D & E Docks & fingers on C Dock

Operations

2. Maintain vessels in Gangplank & Pier 3
3. Relocate E, D & east half of C Dock Boats to X Dock

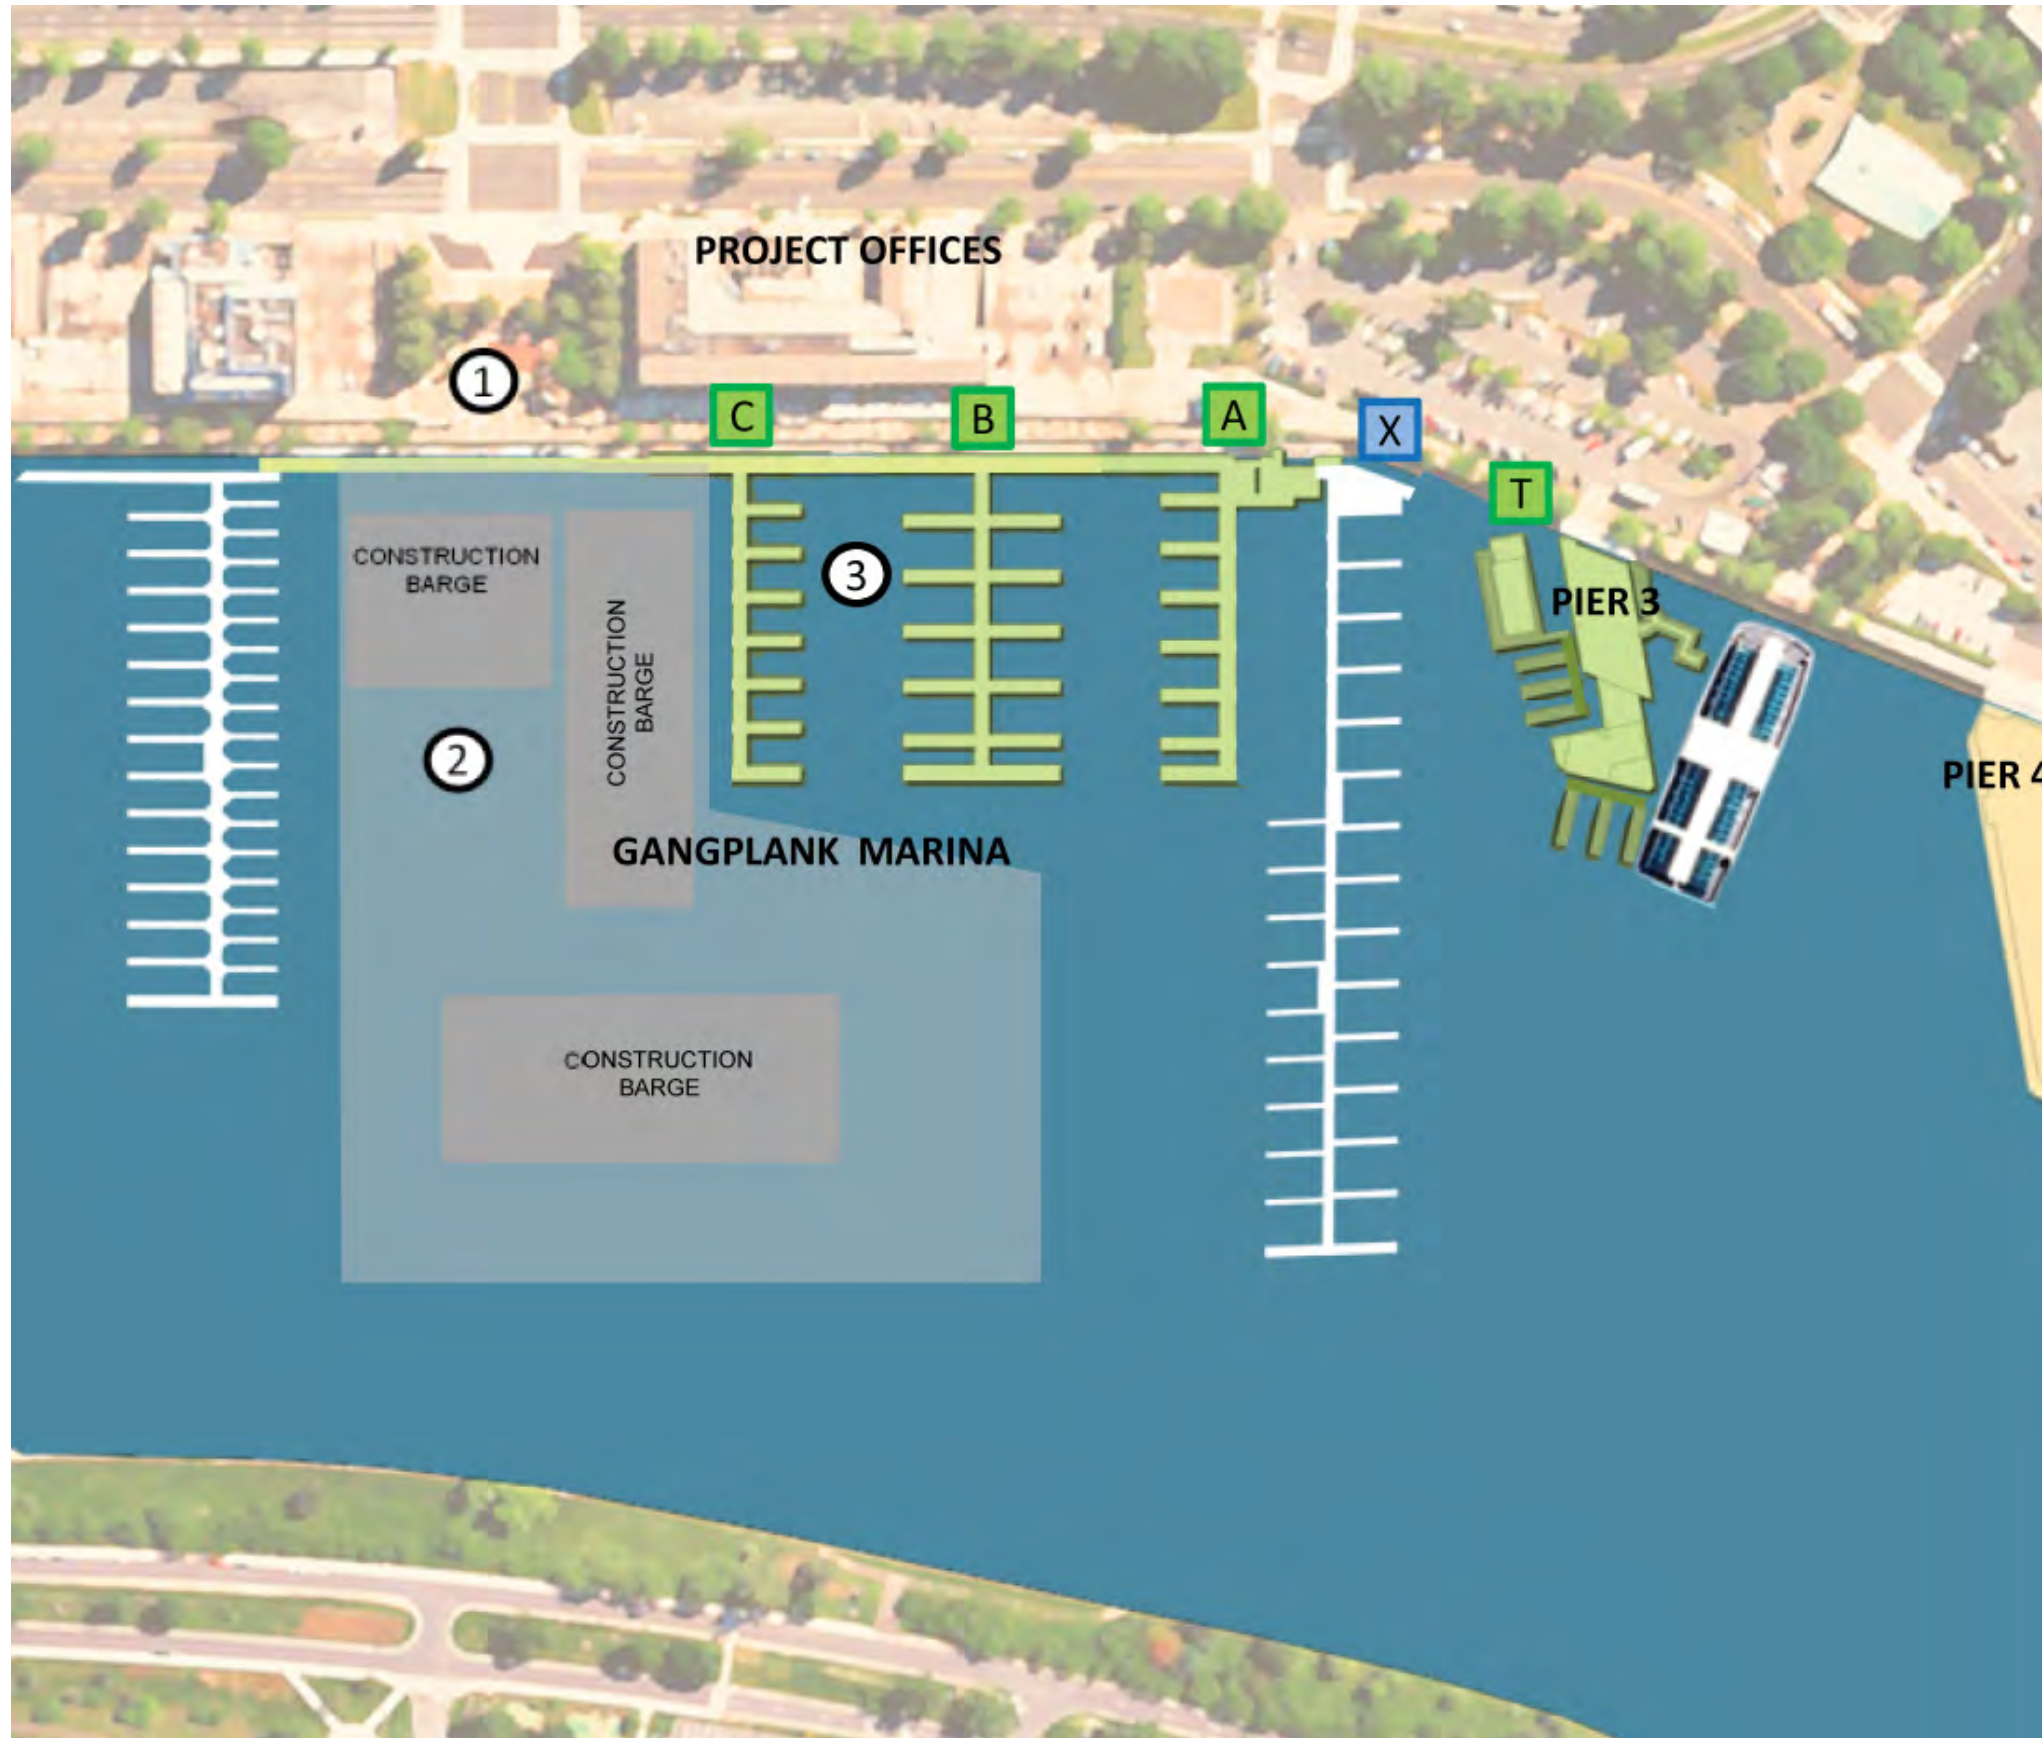


Construction

1. 7th Street Park & Promenade Construction
2. **Recreation Pier & GPM V Dock Construction**

Operations

3. Maintain vessels in Gangplank & Pier 3

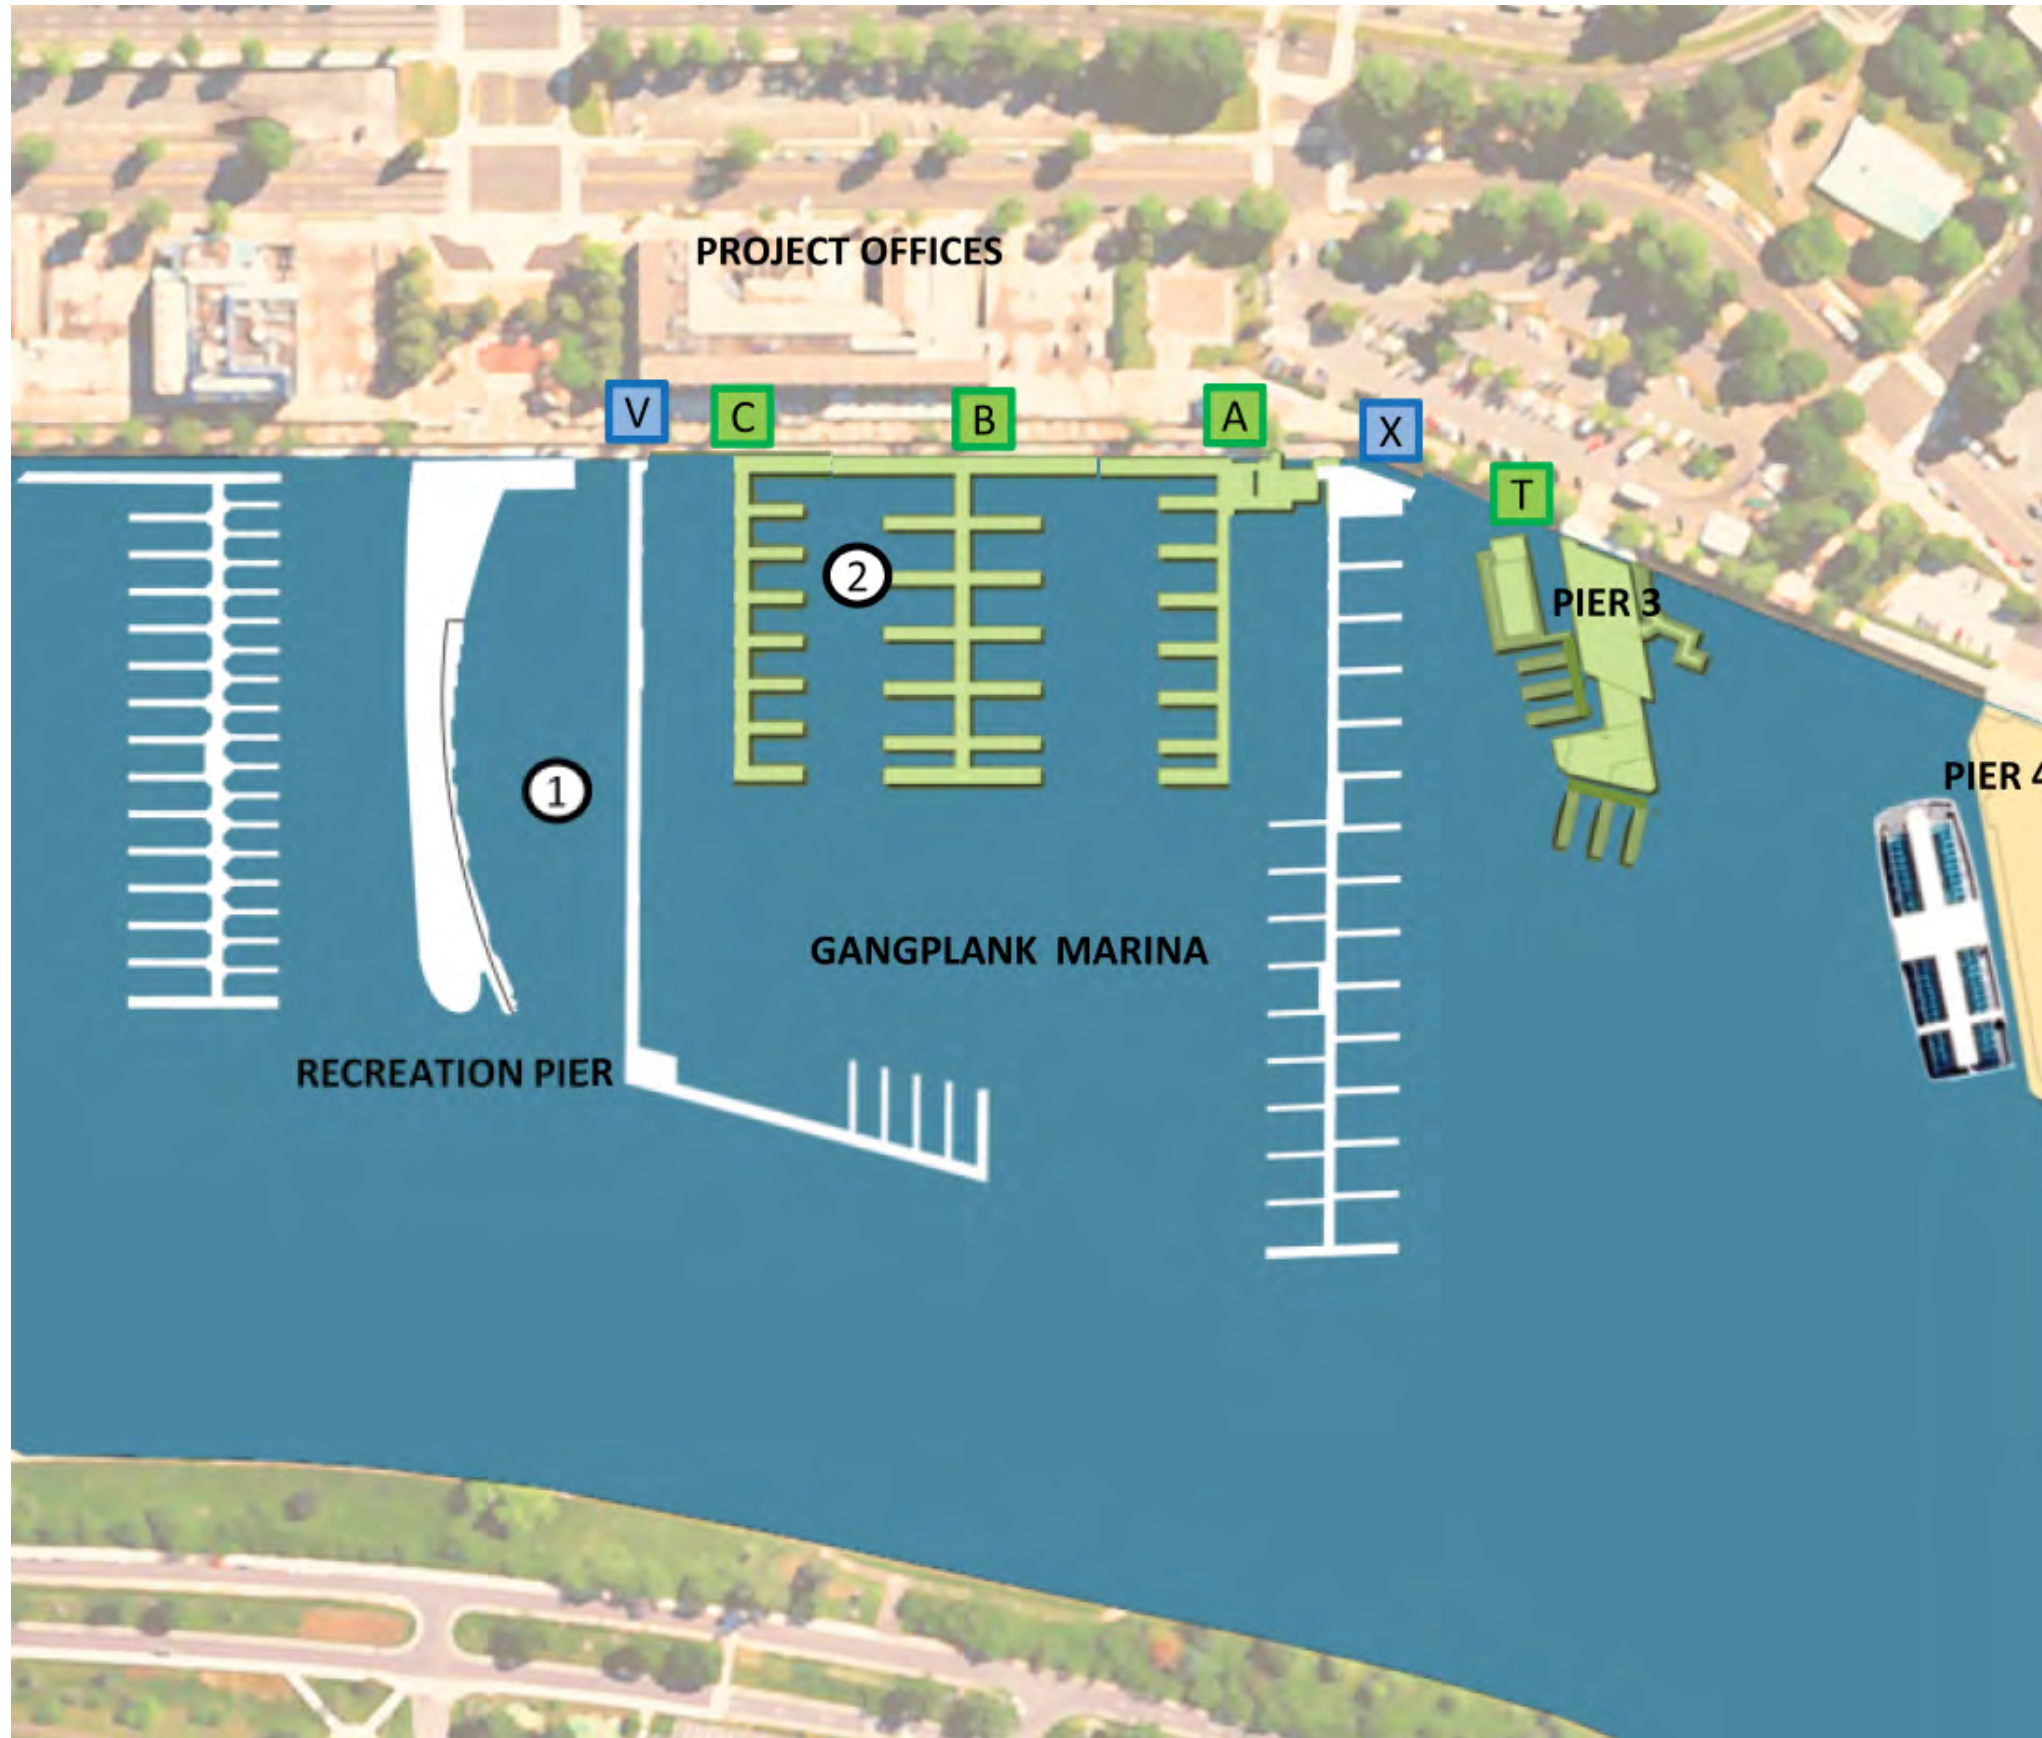


Construction

1. Complete Recreation Pier & GPM V Dock

Operations

2. Maintain vessels at GPM & Pier 3

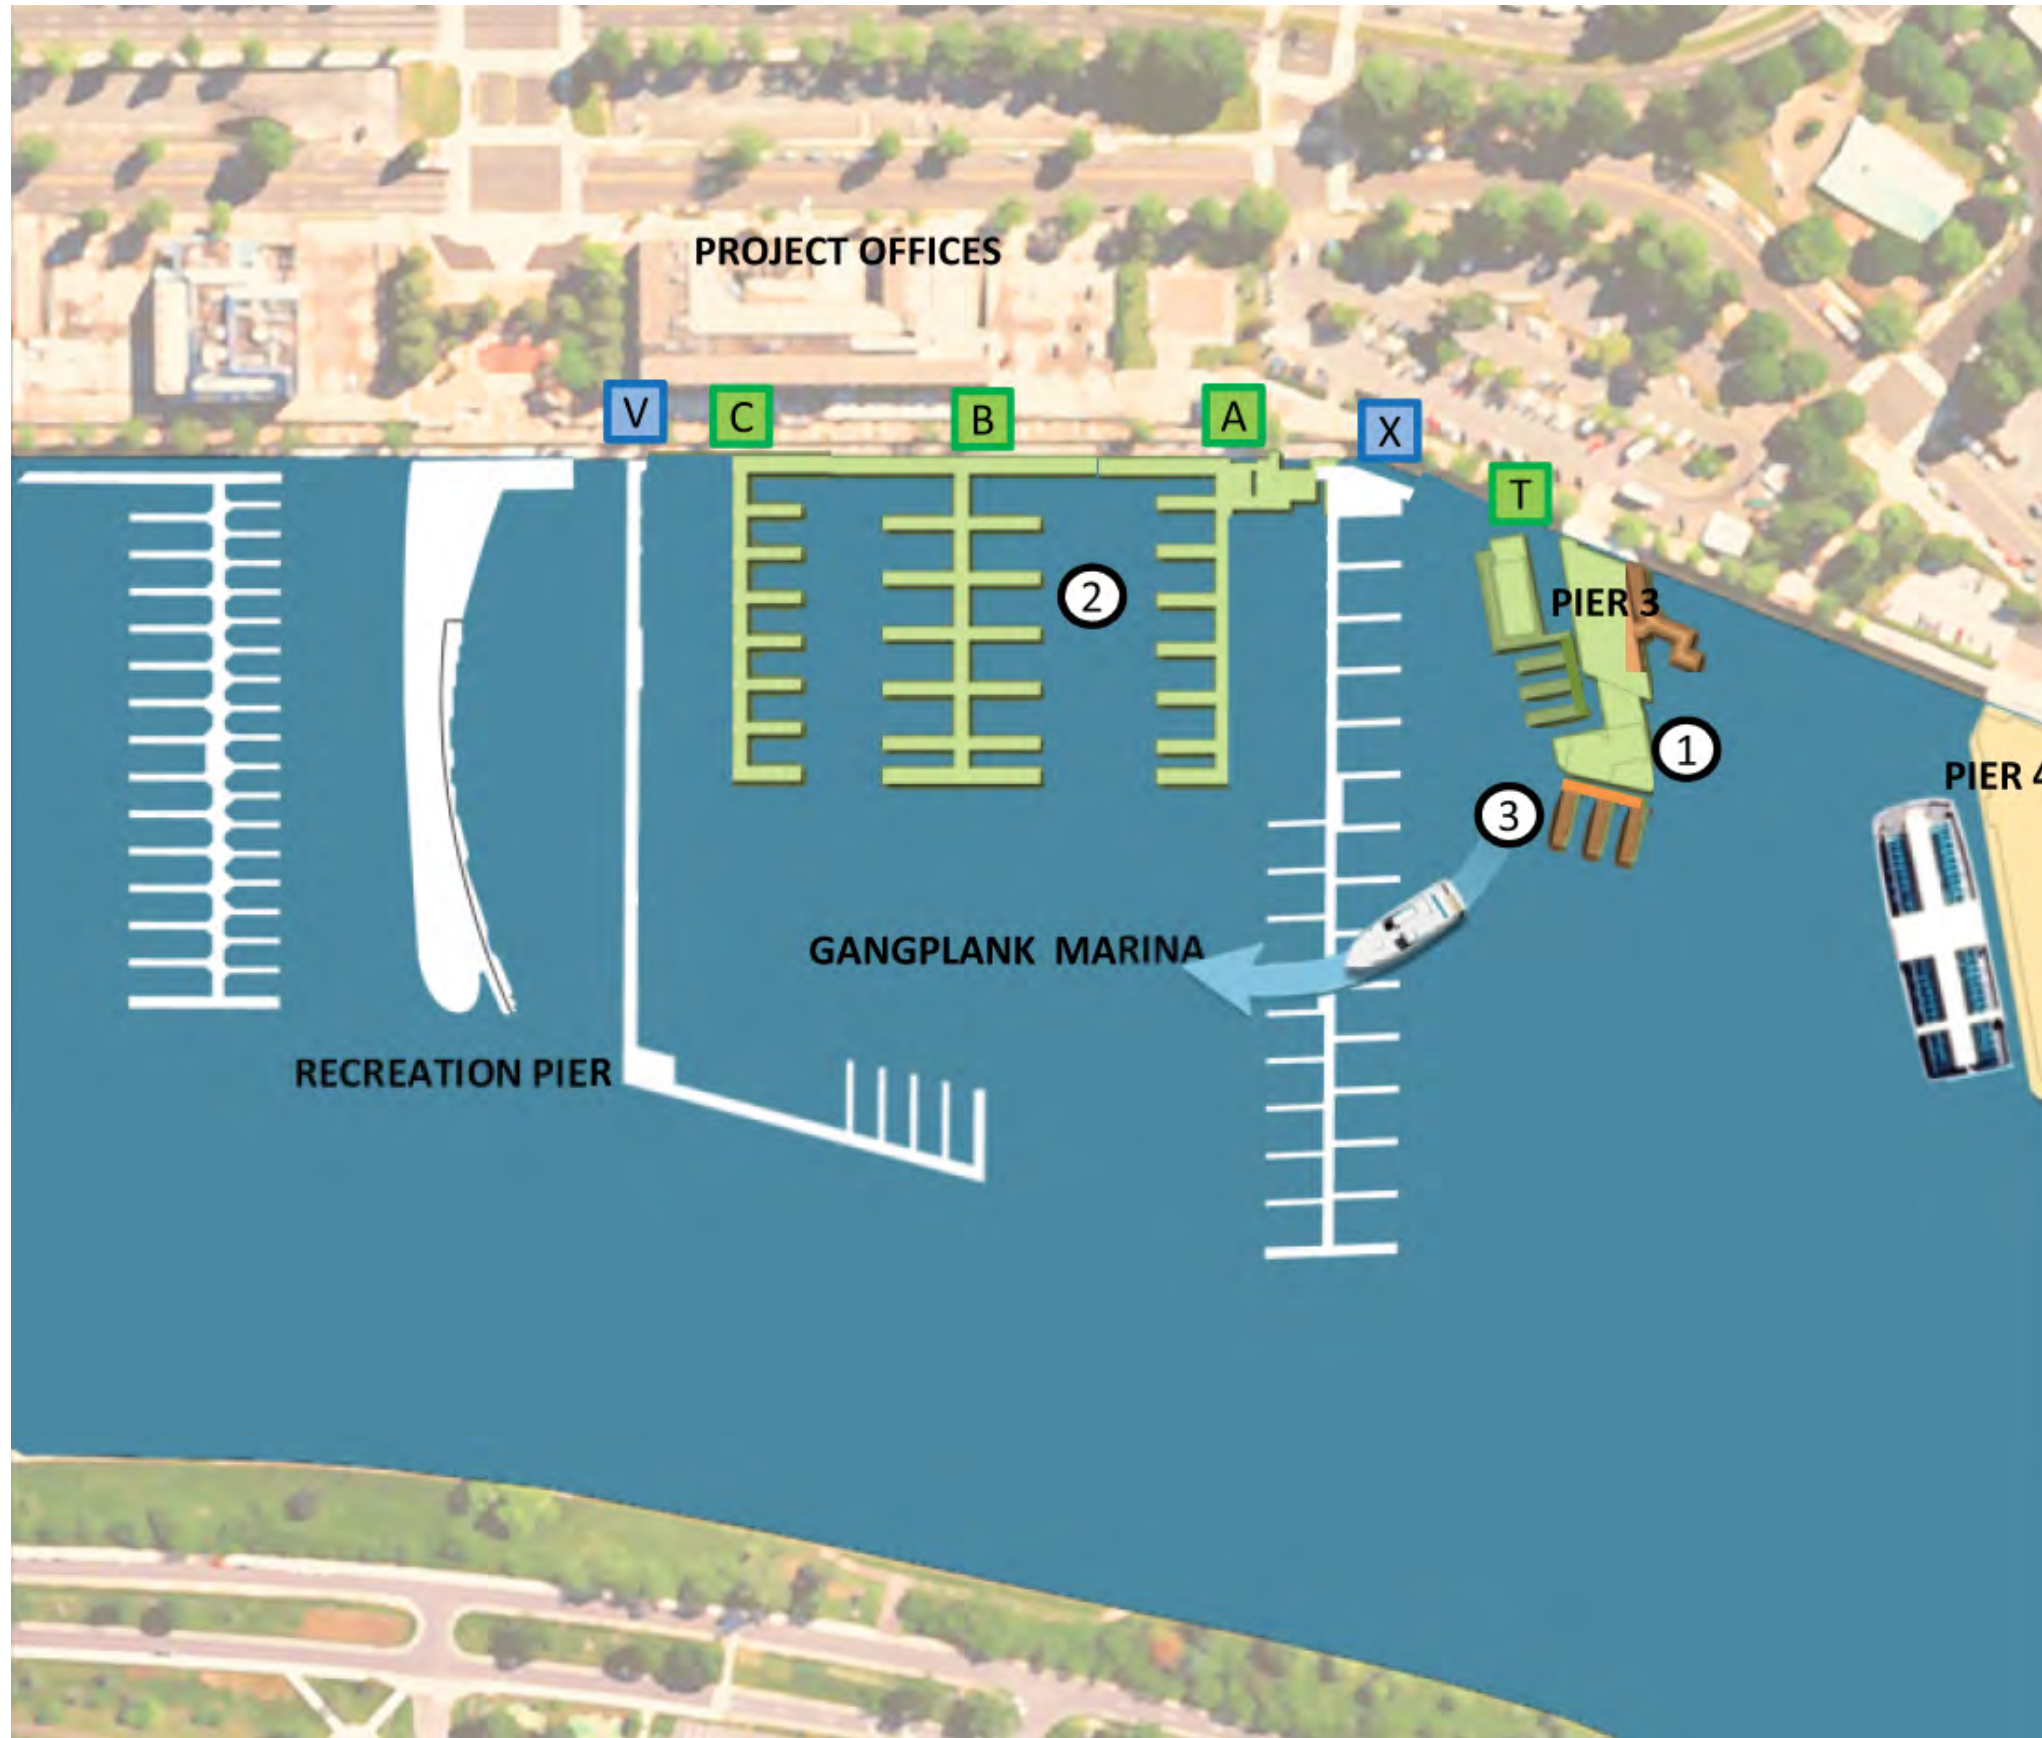


Construction

1. Demo Odyssey Dock & outboard T Dock

Operations

2. Maintain vessels at GPM & Pier 3
3. Relocate outboard T Dock boats to V Dock

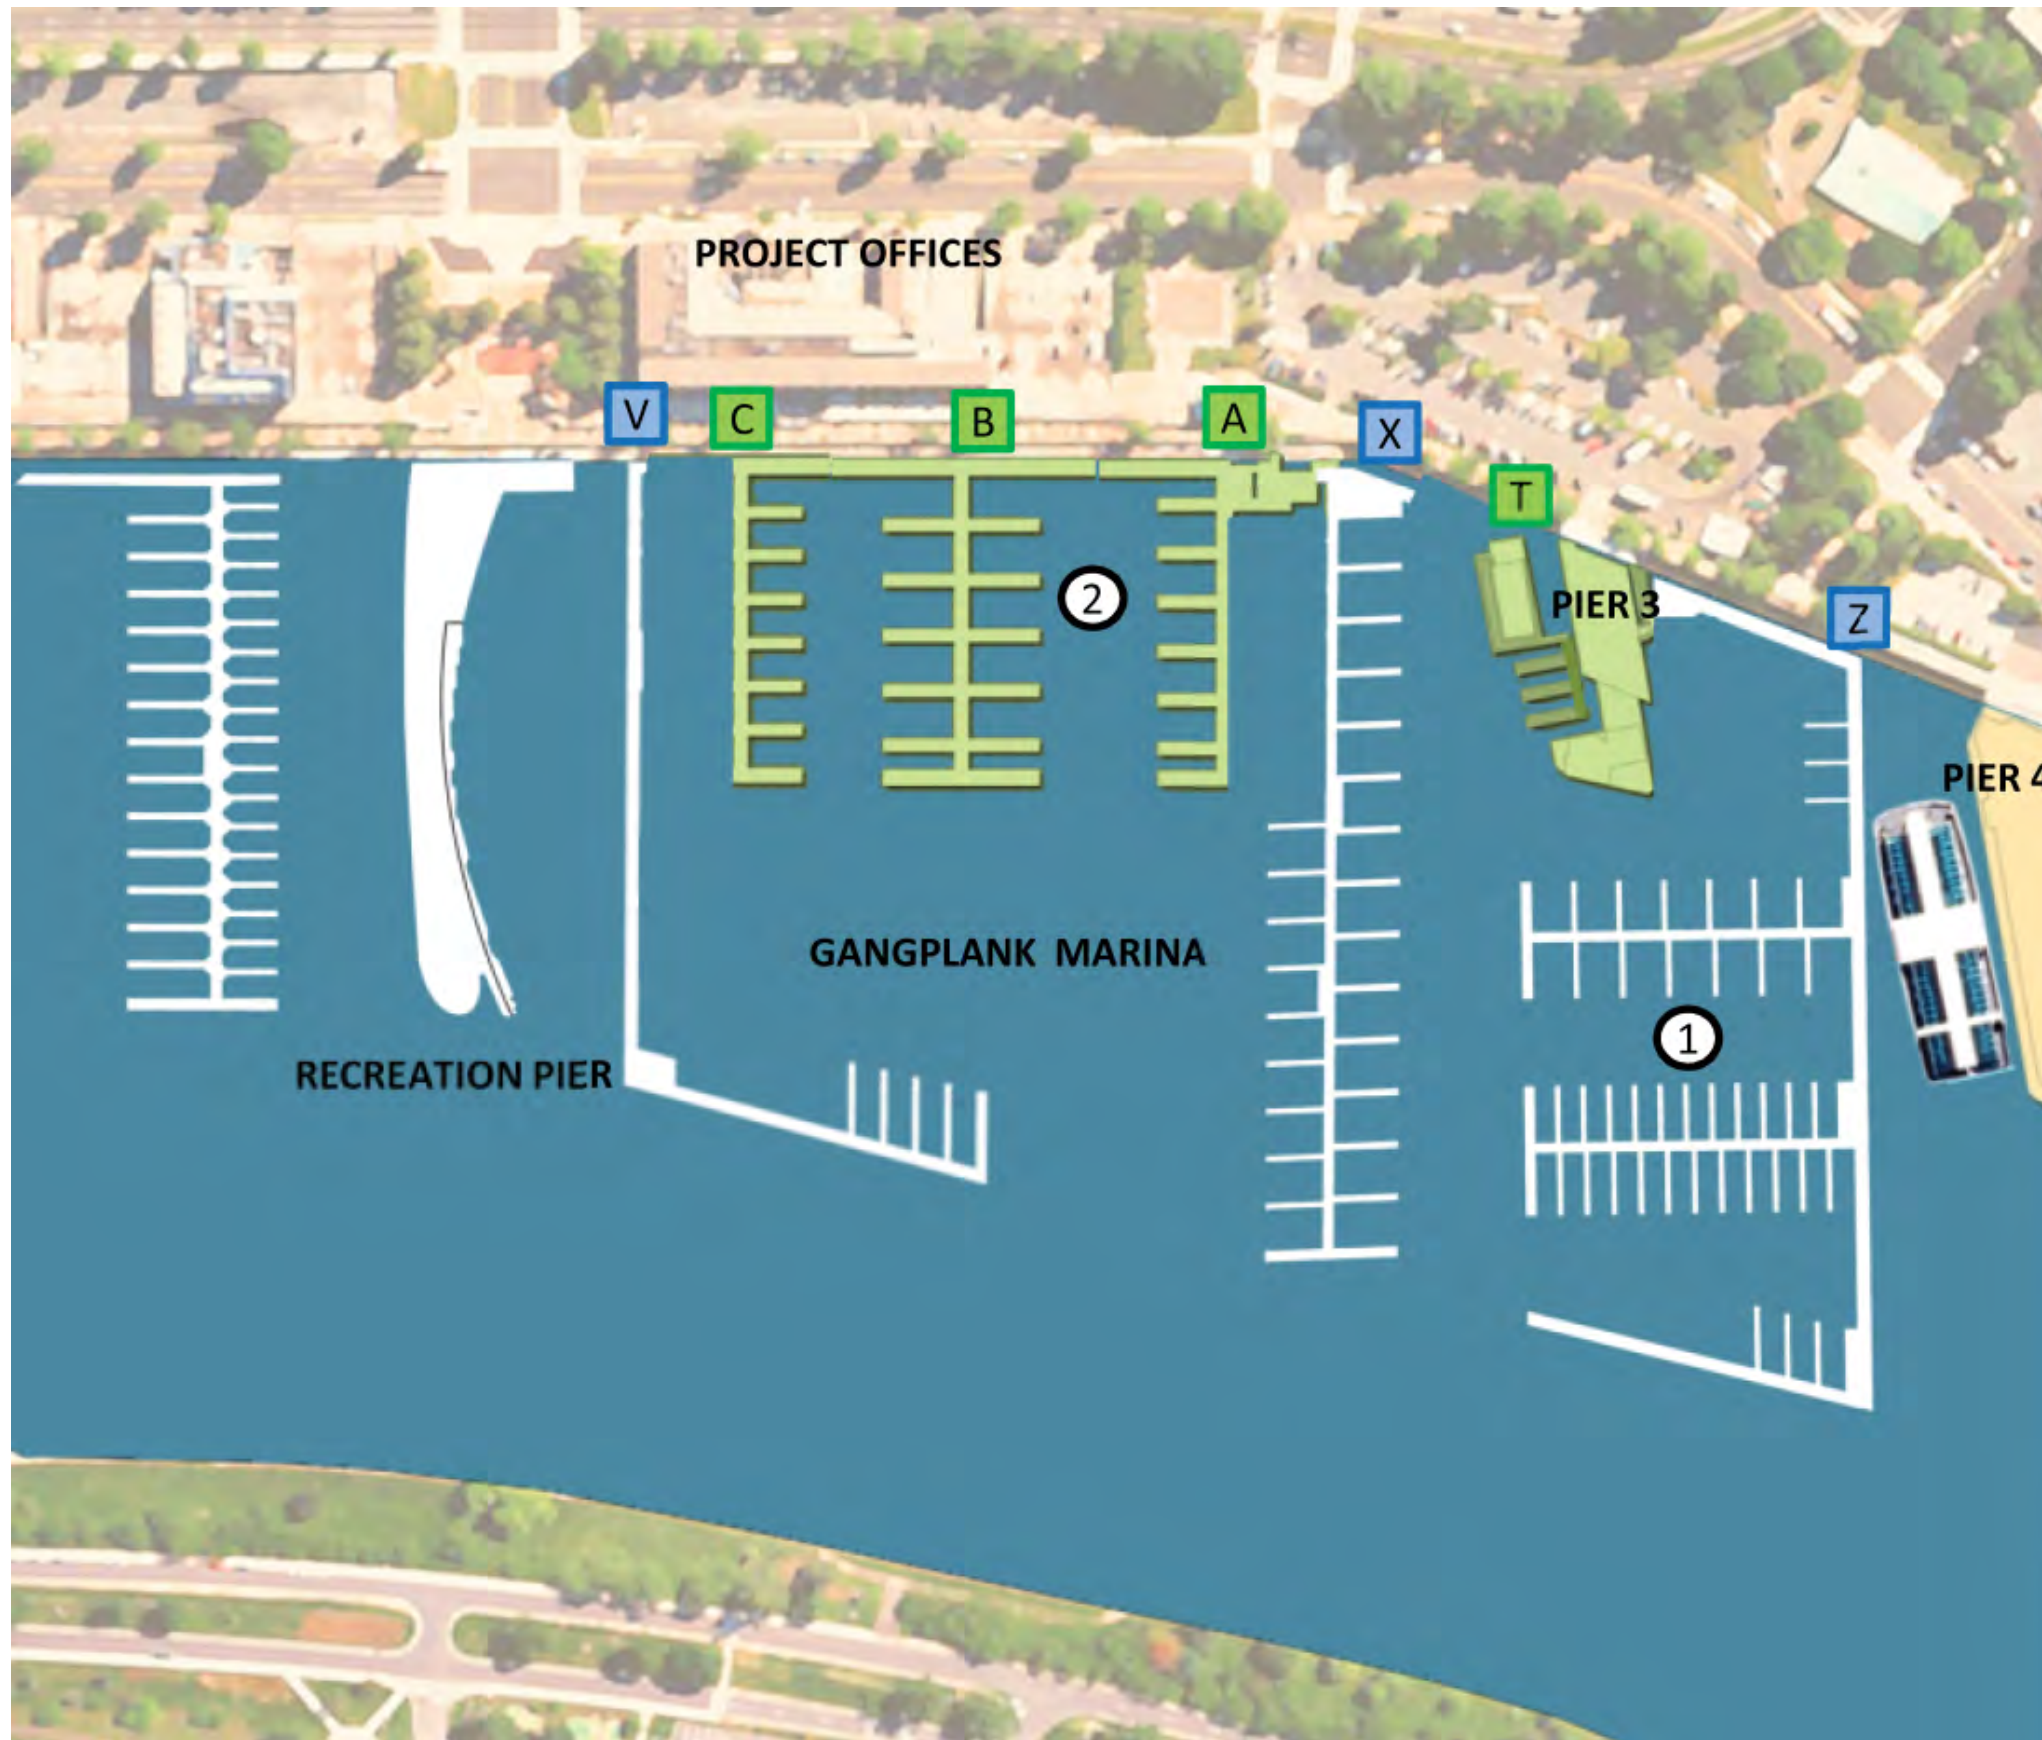


Construction

1. GPM Z Dock Construction

Operations

2. Maintain vessels at GPM & Pier 3

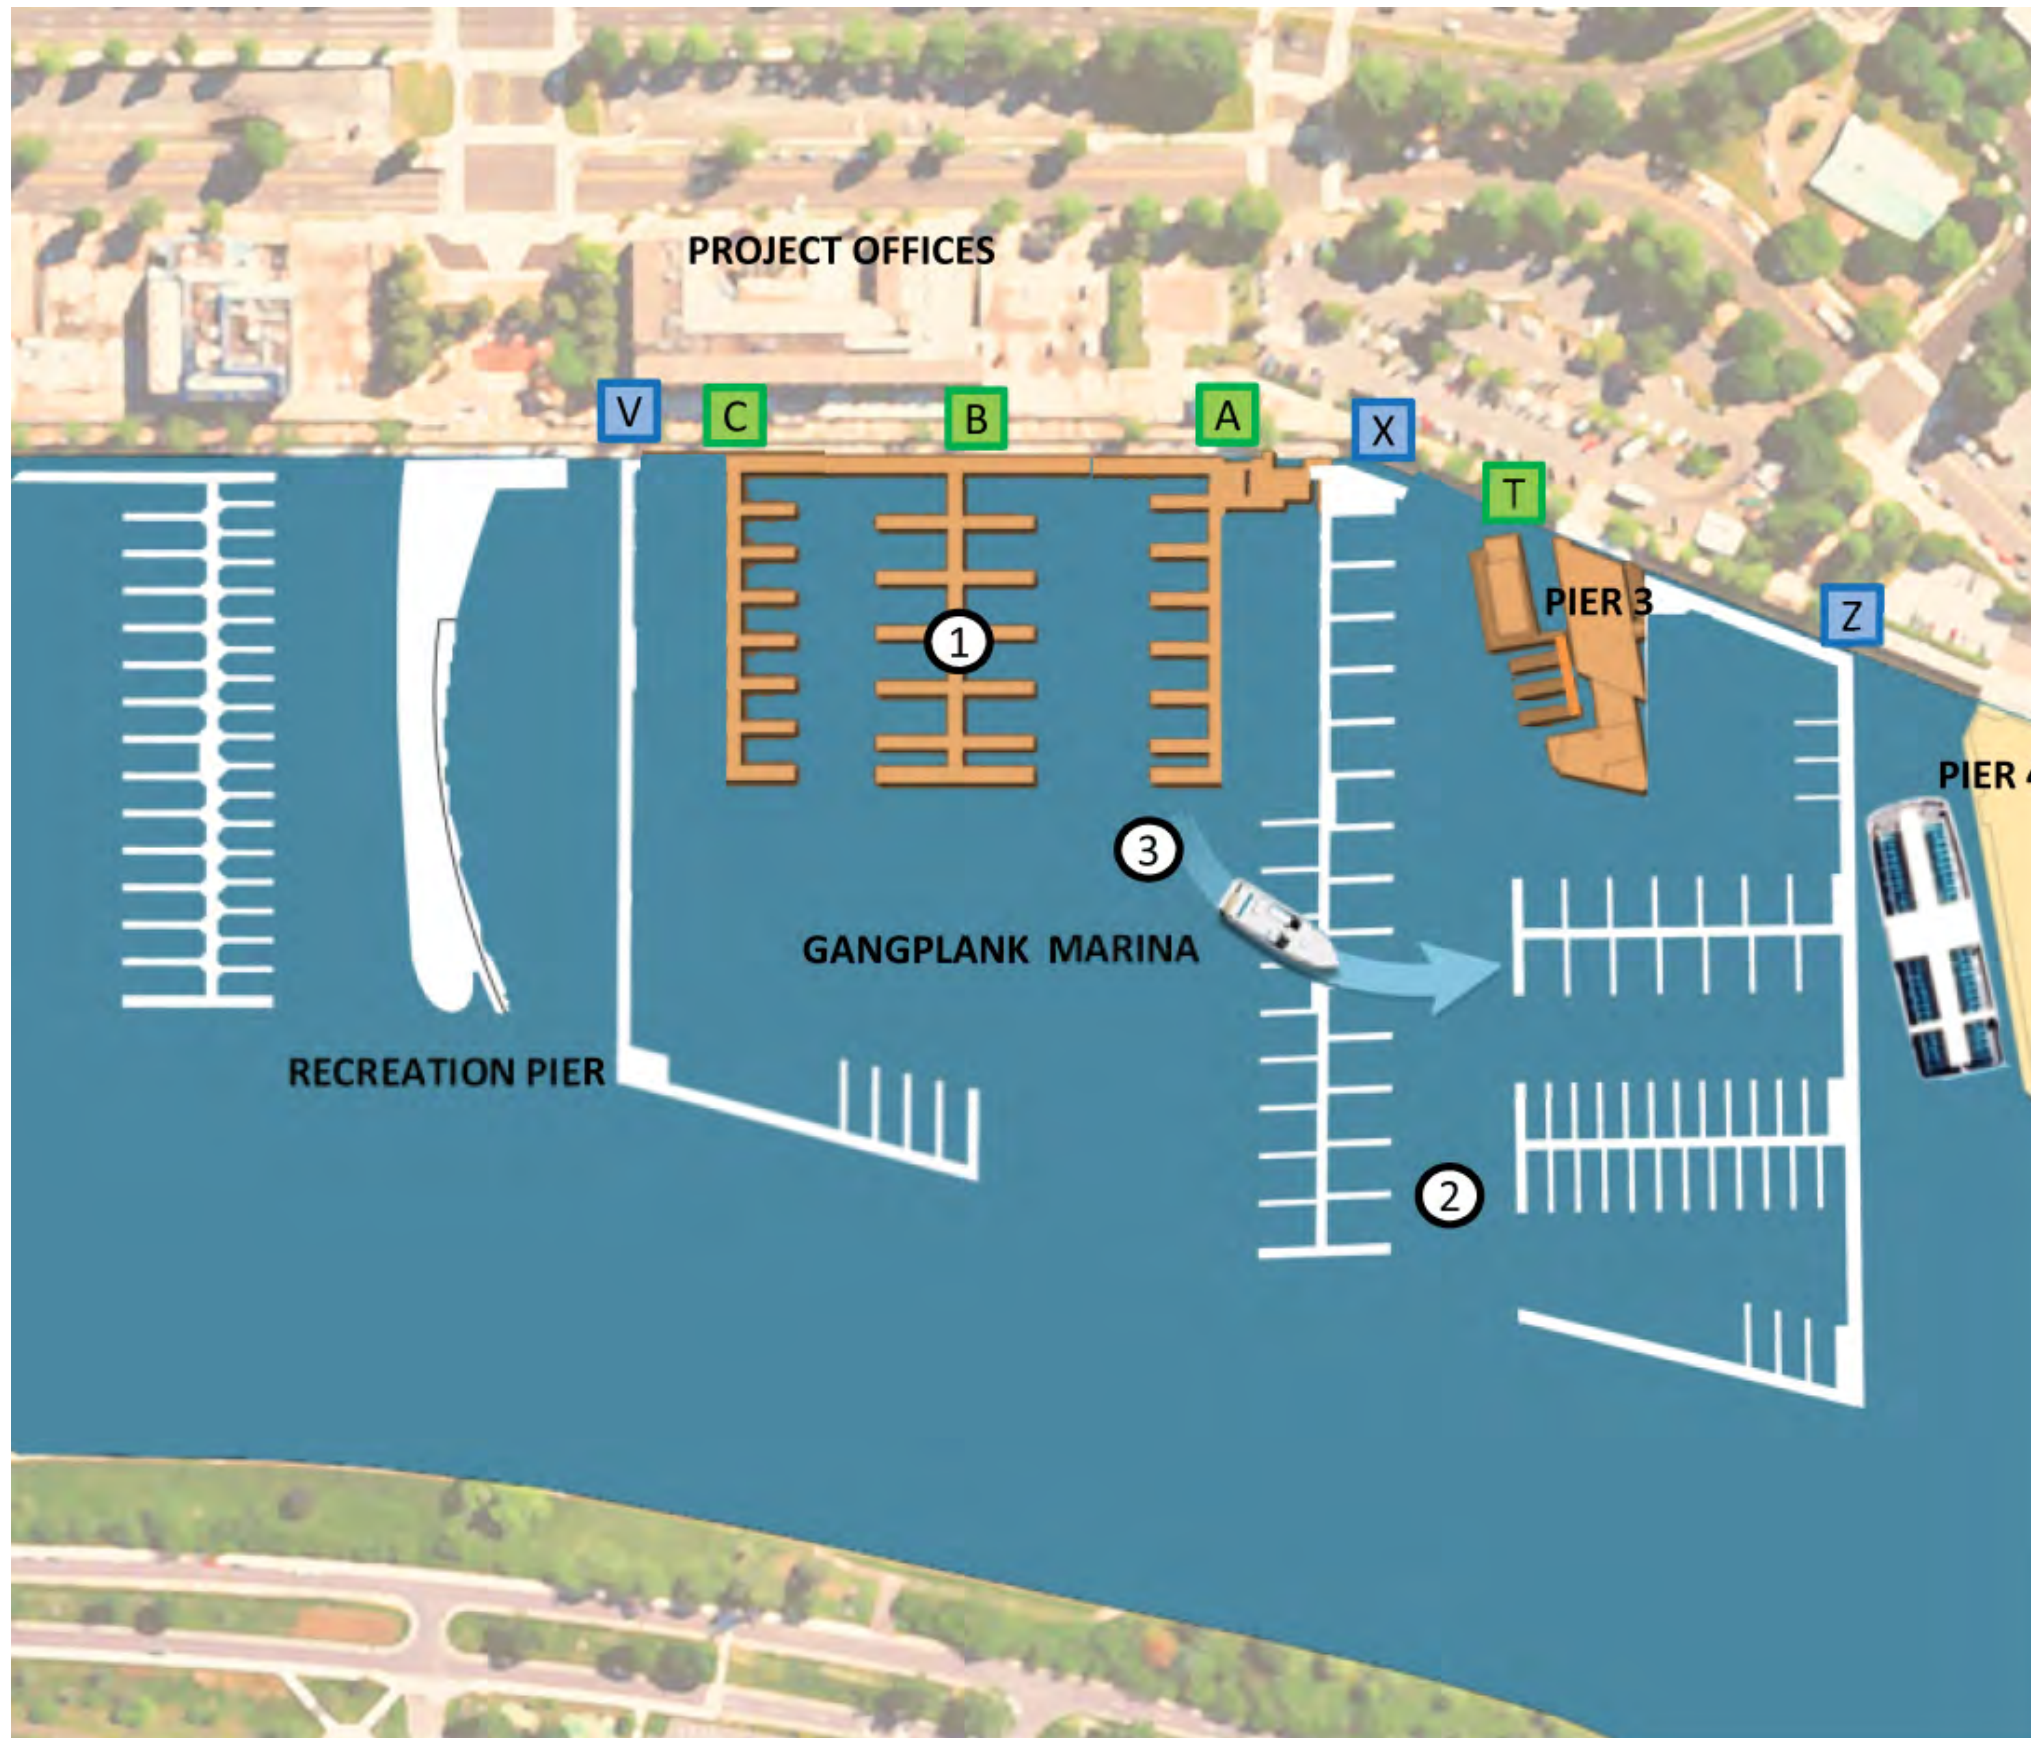


Construction

1. Demo A, B, C & T Docks, Gangplank Pier & Pier 3

Operations

2. Maintain vessels at GPM & Pier 3
3. Relocate A, B, C & T boats to Z Dock

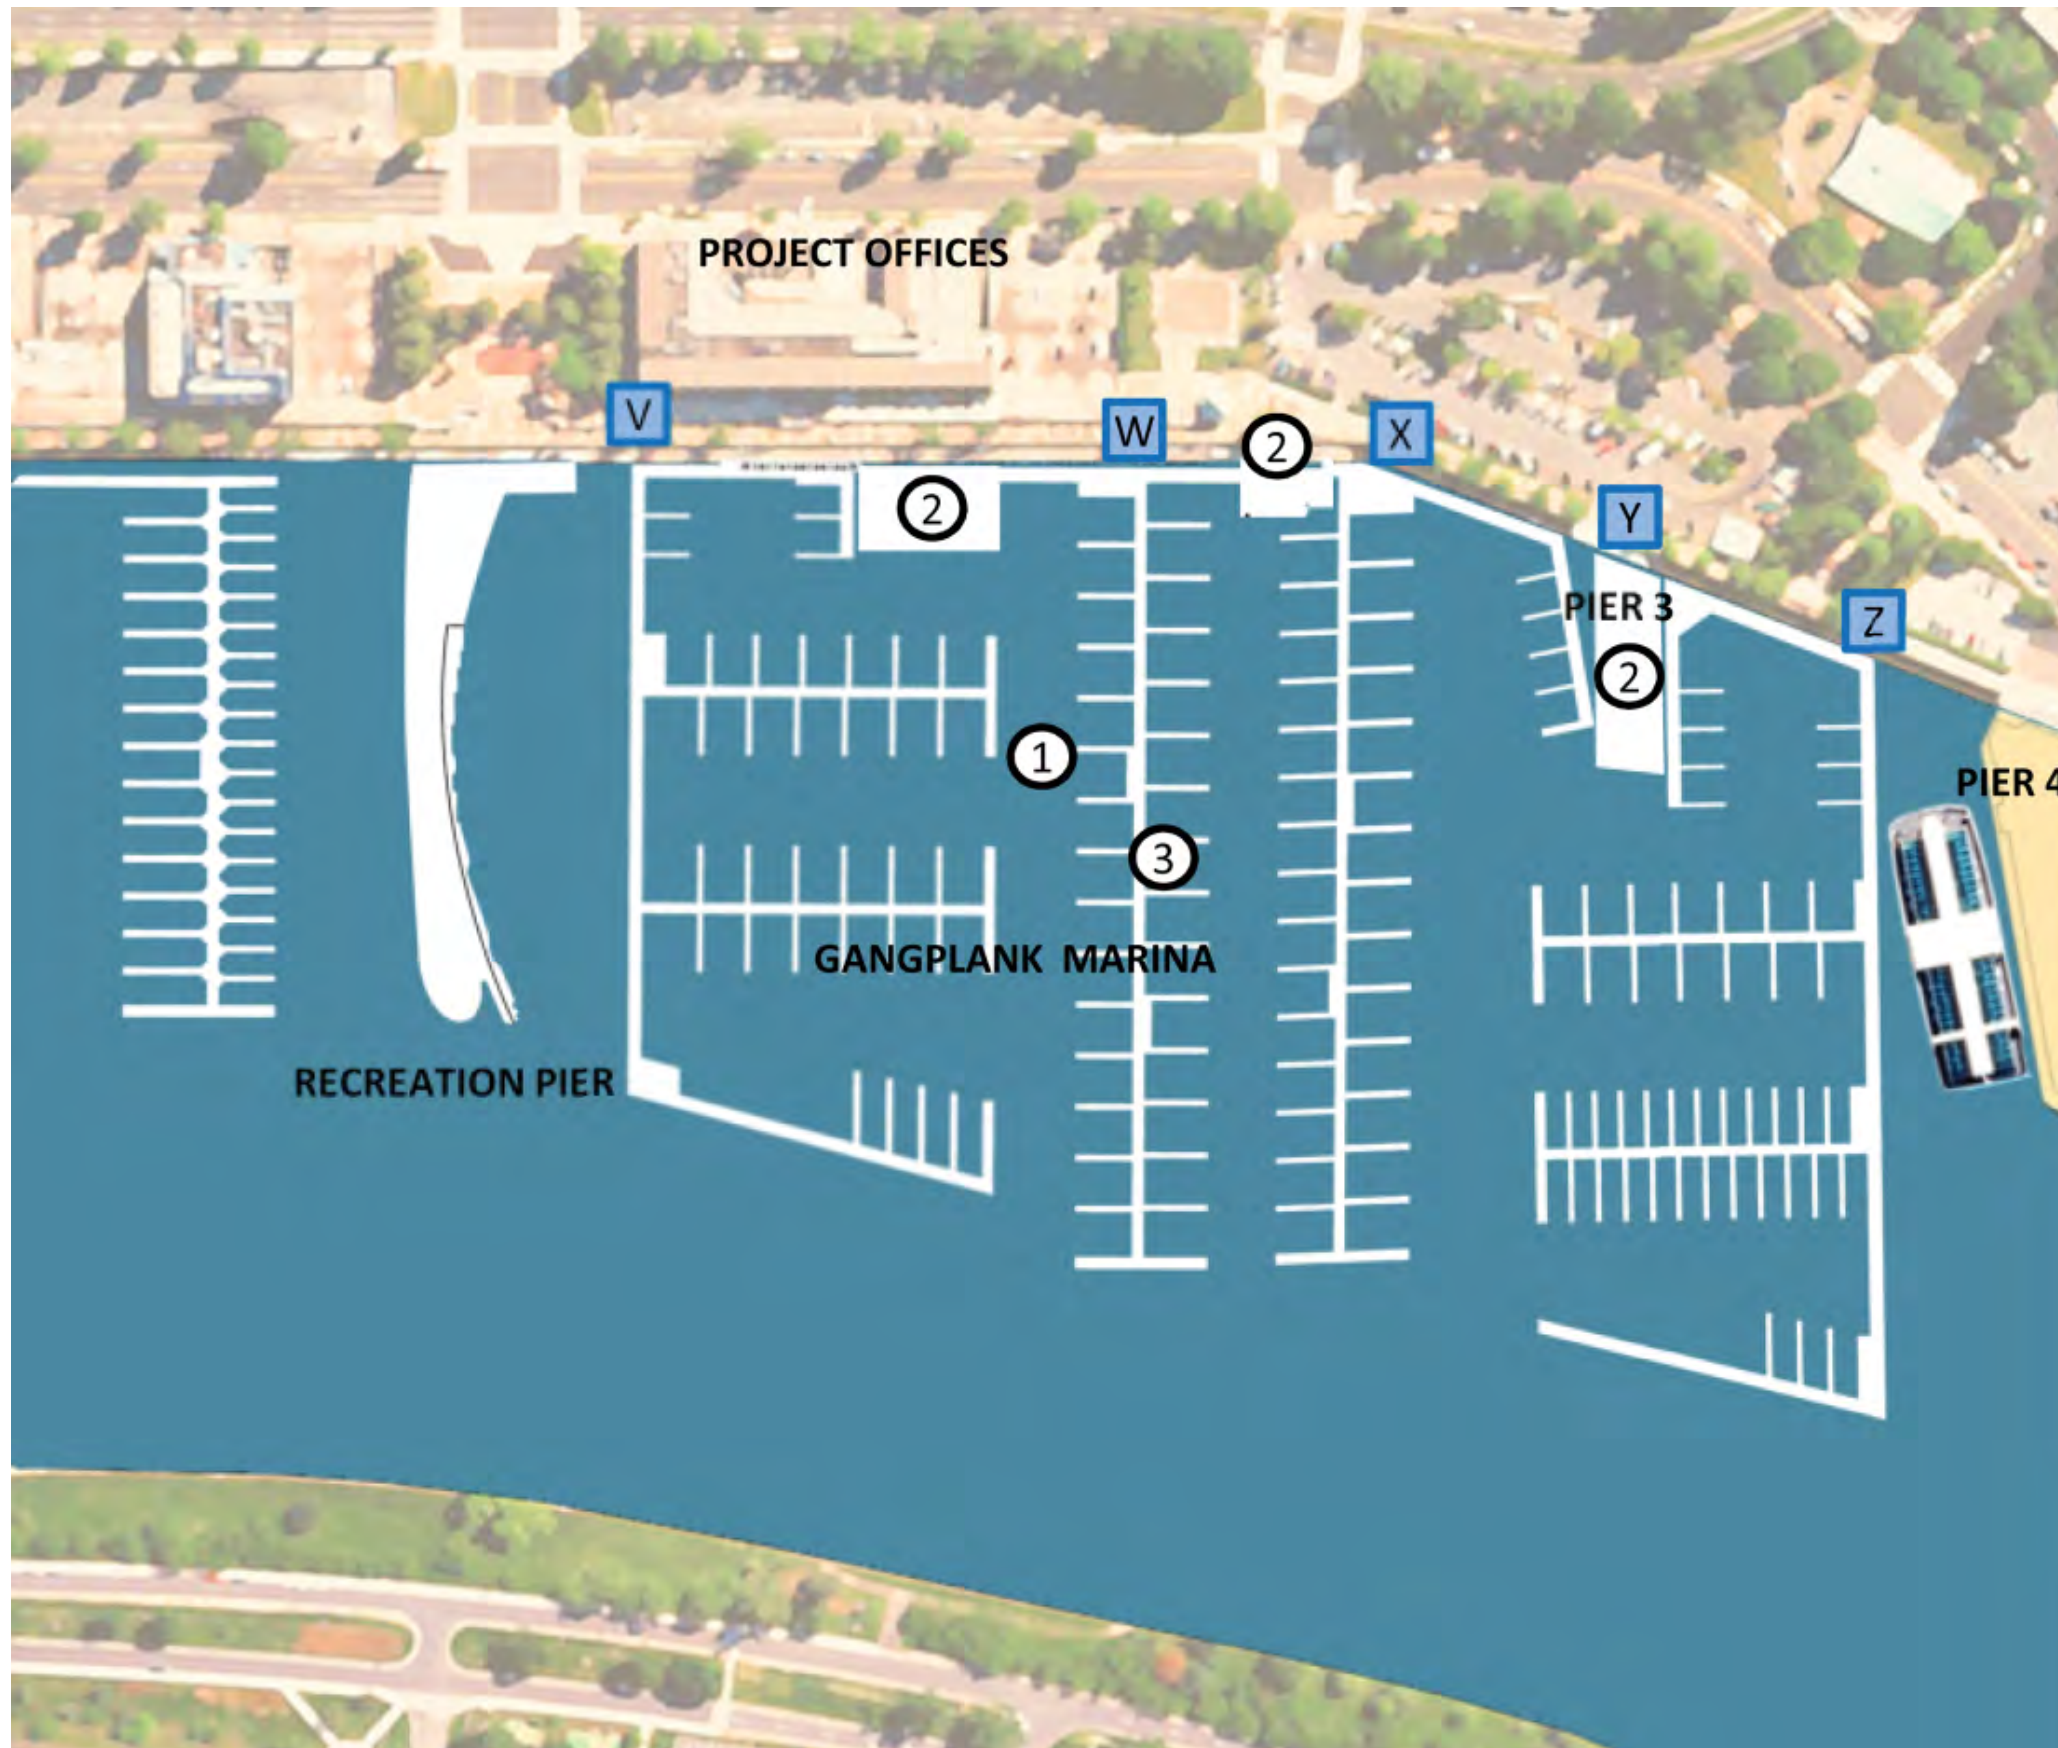

Construction

1. Complete Gangplank Construction
2. Pier 3 & Gangplank Piers Construction/Reconstruction

Operations

3. Maintain vessels at GPM & Pier 3





THE WHARF

HOFFMAN • MADISON WATERFRONT

NOVEMBER 19, 2015

STAGE 2 PUD APPLICATION

MICHAEL VERGASON LANDSCAPE ARCHITECTS, LTD.

