



District Department of Transportation

South Dakota Ave and Riggs Road NE Reconstruction Project

Weekly Status Report Week of 12/2/11 – 12/8/11





Phased Reconstruction of Riggs Road and South Dakota Ave NE Intersection including portions of 3rd Street, Chillum Place, and Kennedy Street NE


Project Summary

Work encompasses:

- Upgraded water mains, storm sewer lines, inlet basins, and sanitary sewer lines
- Repaving road surface and building new brick gutters, and installation of granite curbs
- Sidewalk reconstruction and construction of new driveways
- Safety improvements - crosswalks, wheelchair ramps, and driveway entrances
- New streetlights, upgraded traffic signals, and timing
- Landscaping upgrades

Original contract value: \$7,946,545.41
Prime contractor: Civil Construction, LLC
Notice to Proceed Date: March 1, 2010

Project Financials (as of 12.8.11)

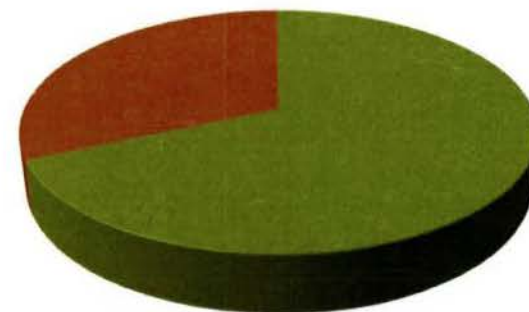

■ Completed to Date (68.53%) ■ Remaining Value (31.47%)



Preparation for new sidewalk on Riggs Road and South Dakota Ave NE



New sidewalk on Riggs Road and South Dakota Ave NE



Installation of the 60-inch storm drain on South Dakota Ave NE



Installation of 60-inch storm drain on South Dakota Ave NE

Issues and Resolutions

The utility conflict between the gas line and storm water system on 3rd Street NE has been resolved. Washington Gas will begin installation of a new gas main.

The conflict between the proposed 15-inch sanitary sewer location and an existing gas line on South Dakota from Kennedy to Riggs Road NE has been resolved.

We have received no further direction regarding the permanent closure of the Riggs Road ramp to South Dakota Ave. We created a temporary work zone to keep the project moving forward.

Community Outreach

We attended the December Lamond Riggs Citizens Association meeting to provide a brief project update and listen to any concerns. We will be back for the February meeting.

We prepared two traffic advisories. One for 3rd Street and the other for Riggs Road NE. In addition, we called the businesses in the area to alert them of the upcoming changes in traffic patterns.

Look Ahead

Riggs Road NE: Removed existing sidewalk and installed new sidewalk on the west corner of Riggs Road and South Dakota NE.

South Dakota Ave NE: Continued installation of the 60-inch storm sewer pipe.

3rd Street NE: No major work performed.

Expected activities include:

- Finish installation of 60-inch storm drain on South Dakota Avenue NE between Kennedy Street and Riggs Road NE.
- Install 15-inch sewer line on South Dakota Ave NE.
- Shift traffic on Riggs Road to remove and install new roadway from South Dakota Ave to the top of the ramp.
- Washington Gas will install new gas main on 3rd Street NE



Intelligent Construction Coordination

Wegman & Co. Drawing, Ltd.

For more information please contact us at

1-800-368-3688 or visit our website at www.wegman.com



District Department of Transportation

South Dakota Ave and Riggs Road NE Reconstruction Project

Weekly Status Report Week of 12/23/11 – 12/29/11





Phased Reconstruction of Riggs Road and South Dakota Ave NE Intersection including portions of 3rd Street, Chillum Place, and Kennedy Street NE


Project Summary

Work encompasses:

- Upgraded water mains, storm sewer lines, inlet basins, and sanitary sewer lines
- Repaving road surface and building new brick gutters, and installation of granite curbs
- Sidewalk reconstruction and construction of new driveways
- Safety improvements - crosswalks, wheelchair ramps, and driveway entrances
- New streetlights, upgraded traffic signals, and timing
- Landscaping upgrades

Original contract value: \$7,946,545.41
Prime contractor: Civil Construction, LLC
Notice to Proceed Date: March 1, 2010

Project Financials (as of 12.29.11)

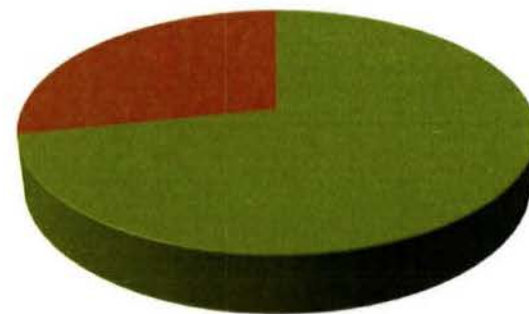

■ Completed to Date (71.78%) ■ Remaining Value (28.22%)



Brickwork for the construction channel on South Dakota Ave NE



Brickwork for the construction channel on South Dakota Ave NE



Saw cutting existing roadway to prepare to excavate for installation of 15-inch sanitary line on South Dakota Ave NE



Installation of shoring system to install 15-inch sanitary line on South Dakota Ave NE

Issues and Resolutions

Washington Gas is currently installing the new gas main on 3rd Street NE. Weather and construction conditions permitting, this should be complete in a month.

We have received no further direction regarding the permanent closure of the Riggs Road ramp to South Dakota Ave. We created a temporary work zone to keep the project moving forward.

Community Outreach

Washington Gas is currently working on 3rd Street NE. We are coordinating with the Washington Gas crew to ensure there is access to the businesses on 3rd Street NE. We communicated directly with the businesses to provide an update.

Look Ahead

Riggs Road NE: No major work performed.

South Dakota Ave NE: Began installation of the 15-inch sewer line on South Dakota Ave NE

3rd Street NE: Washington Gas continued installation of the new gas main.

Expected activities include:

- Continue installing of 15-inch sewer line on South Dakota Ave NE.
- Washington Gas will continue installing new gas main on 3rd Street NE



Project Name: Construction of the New Bridge Structure

Location: Highway 101, Bridge 101

Project Manager: John Doe

Project Number: 101-101



District Department of Transportation

South Dakota Ave and Riggs Road NE Reconstruction Project

Weekly Status Report Week of 12/30/11 – 1/5/12





Phased Reconstruction of Riggs Road and South Dakota Ave NE Intersection including portions of 3rd Street, Chillum Place, and Kennedy Street NE


Project Summary

Work encompasses:

- Upgraded water mains, storm sewer lines, inlet basins, and sanitary sewer lines
- Repaving road surface and building new brick gutters, and installation of granite curbs
- Sidewalk reconstruction and construction of new driveways
- Safety improvements - crosswalks, wheelchair ramps, and driveway entrances
- New streetlights, upgraded traffic signals, and timing
- Landscaping upgrades

Original contract value: \$7,946,545.41
Prime contractor: Civil Construction, LLC
Notice to Proceed Date: March 1, 2010

Project Financials (as of 1.5.12)

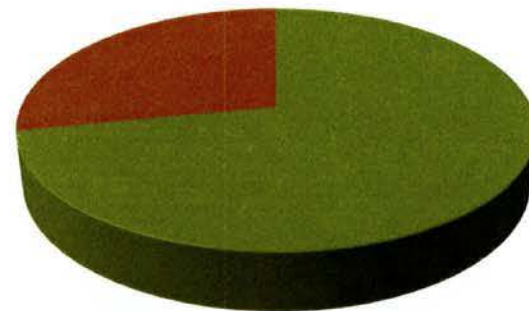

■ Completed to Date (71.91%) ■ Remaining Value (28.09%)




Installing 15-inch sanitary sewer line on South Dakota Ave NE



Washington Gas crew relocating the gas main on 3rd Street NE



Construction of the channel in the storm drain manhole in the intersection of Riggs Road and South Dakota Ave NE

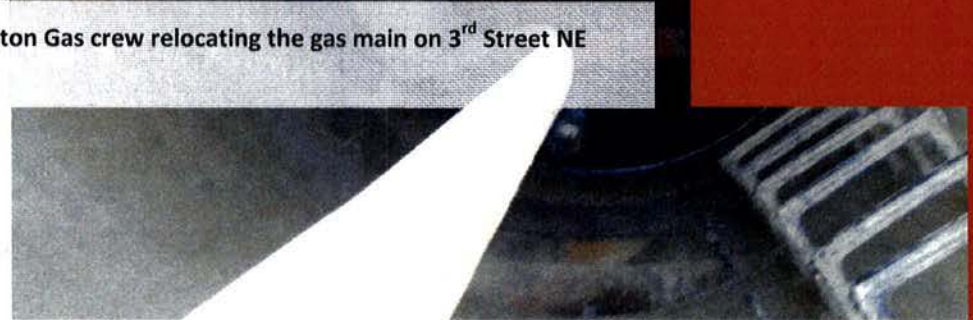

Construction of the channel in the storm drain manhole on Riggs Road NE

Issues and Resolutions

Washington Gas is currently installing the new gas main on 3rd Street NE. Weather and construction conditions permitting, this should be complete in a few weeks.

We have received no further direction regarding the permanent closure of the Riggs Road ramp to South Dakota Ave. We created a temporary work zone to keep the project moving forward.

Community Outreach

Washington Gas is currently working on 3rd Street NE. We are coordinating with the Washington Gas crew to ensure there is access to the businesses on 3rd Street NE. We communicated directly with the businesses to provide an update.

Look Ahead

Riggs Road NE: Hauled project dirt and debris off site

South Dakota Ave NE: Continued installation of the 15-inch sanitary sewer line on South Dakota Ave NE

3rd Street NE: Washington Gas continued installation of the new gas main.

Expected activities include:

- Continue installing of 15-inch sewer line on South Dakota Ave NE.
- Washington Gas will continue installing new gas main on 3rd Street NE



Public Works Construction Coordination

Wendell C. D. Dwyer, P.E.

From the Work area, the following information is

provided to the public:



District Department of Transportation

South Dakota Ave and Riggs Road NE Reconstruction Project

Weekly Status Report Week of 1/6/12 – 1/12/12





Phased Reconstruction of Riggs Road and South Dakota Ave NE Intersection including portions of 3rd Street, Chillum Place, and Kennedy Street NE


Project Summary

Work encompasses:

- Upgraded water mains, storm sewer lines, inlet basins, and sanitary sewer lines
- Repaving road surface and building new brick gutters, and installation of granite curbs
- Sidewalk reconstruction and construction of new driveways
- Safety improvements - crosswalks, wheelchair ramps, and driveway entrances
- New streetlights, upgraded traffic signals, and timing
- Landscaping upgrades

Original contract value: \$7,946,545.41
 Prime contractor: Civil Construction, LLC
 Notice to Proceed Date: March 1, 2010

Project Financials (as of 1.12.12)

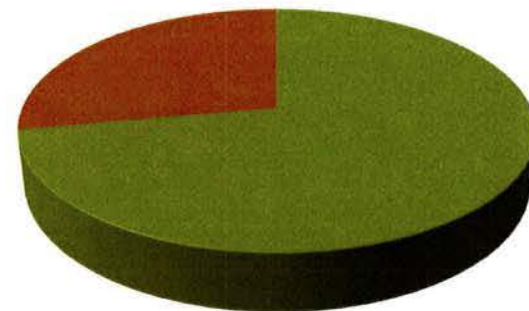

■ Completed to Date (72.05%) ■ Remaining Value (27.95%)



Washington Gas crew relocation the gas main on 3rd Street NE



Installation of light poles on Riggs Road NE



Construction brick channel inside manhole on South Dakota Ave NE



Installation of sewer manhole on South Dakota Ave NE

Issues and Resolutions

Washington Gas is currently installing the new gas main on 3rd Street NE. Weather and construction conditions permitting, this should be complete in a few weeks.

We had a new utility conflict on South Dakota Ave NE. The issue was the elevation of the sewer line so the water flows. It was resolved quickly.

We have received no further direction regarding the permanent closure of the Riggs Road ramp to South Dakota Ave. We created a temporary work zone to keep the project moving forward.

Community Outreach

Washington Gas is currently working on 3rd Street NE. We are coordinating with the Washington Gas crew to ensure there is access to the businesses on 3rd Street NE. We communicated directly with the businesses to provide an update.

Look Ahead

Riggs Road NE: Construction of brick channel in manhole. Installation of light poles near Food & Friends. Continued to haul dirt off the project site.

South Dakota Ave NE: Continued installation of the 15-inch sanitary sewer line on South Dakota Ave NE

3rd Street NE: Washington Gas continued installation of the new gas main.

Expected activities include:

- Continue installing of 15-inch sewer line on South Dakota Ave NE.
- Washington Gas will continue installing new gas main on 3rd Street NE



Investigation of the failure of the concrete structure

Washington, D.C. 20001

The following work was performed for the purpose of the investigation

1. Investigation of the failure of the concrete structure
