



District Department of Transportation

South Dakota Ave and Riggs Road NE Reconstruction Project

Weekly Status Report Week of 4/27/12 – 5/3/12



Board of Zoning Adjustment
District of Columbia
CASE NO. 120005
EXHIBIT NO. 5555



Phased Reconstruction of Riggs Road and South Dakota Ave NE Intersection including portions of 3rd Street, Chillum Place, and Kennedy Street NE


Project Summary


Work encompasses:

- Upgraded water mains, storm sewer lines, inlet basins, and sanitary sewer lines
- Repaving road surface and building new brick gutters, and installation of granite curbs
- Sidewalk reconstruction and construction of new driveways
- Safety improvements - crosswalks, wheelchair ramps, and driveway entrances
- New streetlights, upgraded traffic signals, and timing
- Landscaping upgrades


Original contract value: \$7,946,545.41
Prime contractor: Civil Construction, LLC
Notice to Proceed Date: March 1, 2010

Project Financials (as of 5.3.12)

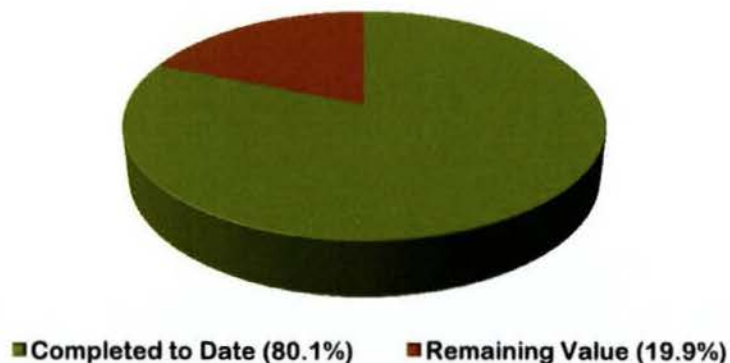


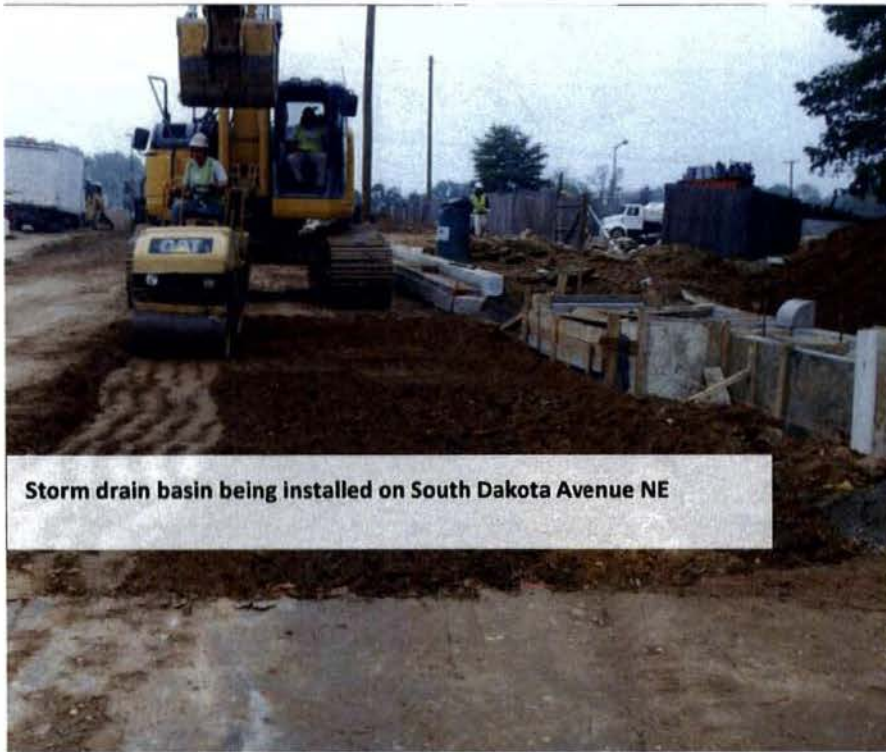

Storm drain basin being installed on South Dakota Avenue NE



Removing exiting roadway on South Dakota Avenue NE

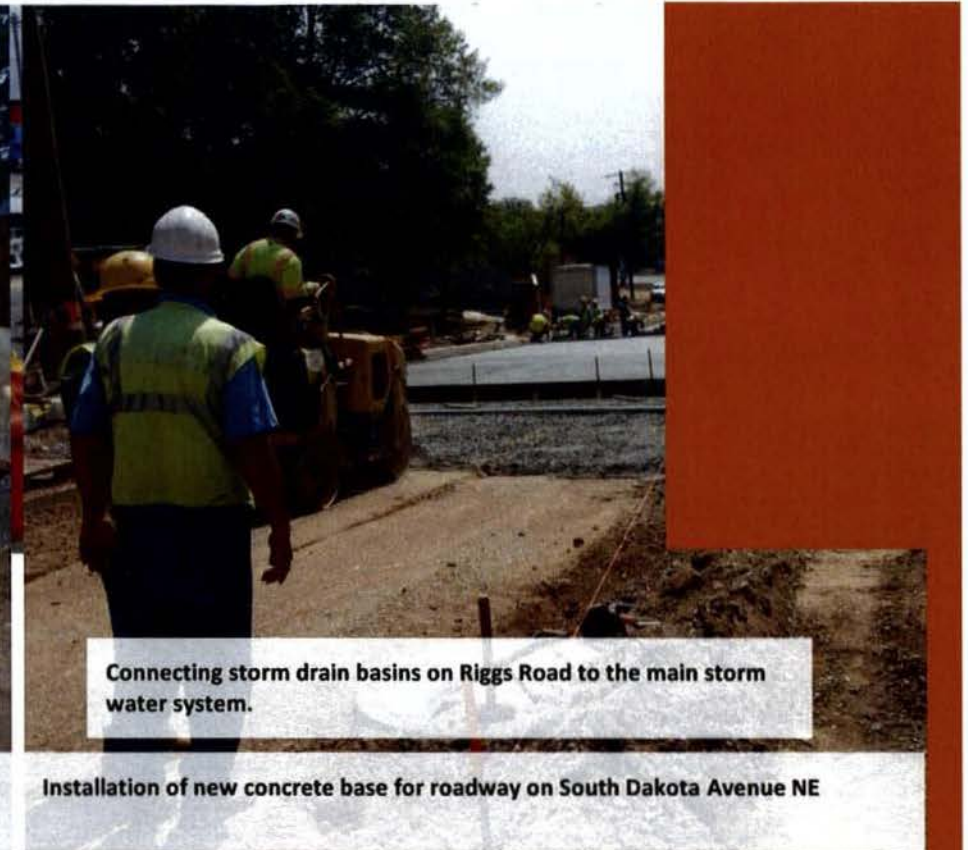

Connecting storm drain basins on Riggs Road to the main storm water system.

Installation of new concrete base for roadway on South Dakota Avenue NE

Work Performed

Riggs Road NE: Continued installation of sewer line, including excavation and shoring. Connected storm drain basins to main storm water system.

South Dakota Avenue NE: Removed existing roadway and began pour concrete roadway base. Continued installed brick gutter.

3rd Street NE: Installed concrete roadway base. Removed and replaced a defective sidewalk. Installed electrical conduit.

Two-Week Look Ahead

Expected activities include:

- Traffic pattern shift on 3rd Street to complete median and installed concrete roadway base.
- Tie water main into existing water system on Chillum Place NE. We will coordinate with WMATA to detour the E-route.
- Continued installation of brick gutter on Riggs Road NE
- Continued installation of 15-inch sanitary sewer on Riggs Road NE.



Public Outreach Coordinator

Veronica O. Davis, P.E.

Email: Vdavis@nspiregreen.com

Office: 202-450-5267

Cell: 202-695-2160

Issues and Resolutions

All the utility conflicts have been resolved. We have no issues on-site right now.

Community Outreach

We were in attendance at the South Manor Neighborhood Association Meeting on Wednesday May 2, 2012. We provided an update and answered questions. We did not have any items requiring additional follow-up. We will attend the Lamond Riggs Citizens Association meeting on Monday May 7, 2012.

We have a traffic pattern shift coming up, so in the coming week we will be meeting with the businesses in the area of the shift.
